
Main decommissioning work and steps

Fuel removal from the spent fuel pool was completed in December 2014 at Unit 4 and on February 28, 2021 at Unit 3. Work continues sequentially toward the start of fuel removal from Units 1 and 2 and debris (Note 1) retrieval from Units 1-3.



(Note 1) Fuel assemblies having melted through in the accident.

Fuel removal from the spent fuel pool

Fuel removal from the spent fuel pool started from April 15, 2019 at Unit 3 and the removal of all fuel assemblies was completed on February 28, 2021.



Fuel removal (566th assembly) (February 26, 2021) Removed fuel (assemblies)

566/566 (Fuel removal completed on February 28, 2021)

Contaminated water management – triple-pronged efforts -


- (1) Efforts to promote contaminated water management based on the three basic policies
- ① "Remove" the source of water contamination ② "Redirect" fresh water from contaminated areas
- ③ "Retain" contaminated water from leakage
- Strontium-reduced water from other equipment is being re-treated in the multi-nuclide removal equipment (ALPS) and stored in welded-joint tanks.
- Multi-layered contaminated water management measures, including land-side impermeable walls and sub-drains, have stabilized the groundwater at a low level and the increased contaminated water generated during rainfall is being suppressed by repairing damaged portions of building roofs, facing onsite, etc. Through these measures, the generation of contaminated water was reduced from approx. 540 m³/day (in May 2014) to approx. 180 m³/day (in FY2019) and approx. 140 m³/day (in 2020).
- Measures continue to further suppress the generation of contaminated water to 100 m3/day or less within 2025.

(2) Efforts to complete stagnant water treatment

- To lower the stagnant water levels in buildings as planned, work to install additional stagnant
 water transfer equipment is underway. At present, the floor surface exposure condition can be
 maintained except for the Unit 1-3 Reactor Buildings, Process Main Building and the High
 Temperature Incinerator Building.
- In 2020, treatment of stagnant water in buildings was completed, except for the Unit 1-3 Reactor Buildings, Process Main Building and High-Temperature Incinerator Building. For Reactor Buildings, the amount of stagnant water there will be reduced to about half of the amount at the end of 2020 during the period FY2022-2024.
- For Zeolite sandbags on the basement floors of the Process Main Building and High-Temperature Incinerator Building, measures to reduce the radiation dose are being examined with stabilization in mind.

(3) Efforts to stably operate contaminated water management

To prepare for tsunamis, various measures are underway. For heavy rain, sandbags are being
installed to suppress direct inflow into buildings while work closing building openings and
installing sea walls to enhance drainage channels and other measures are being implemented as
planned.

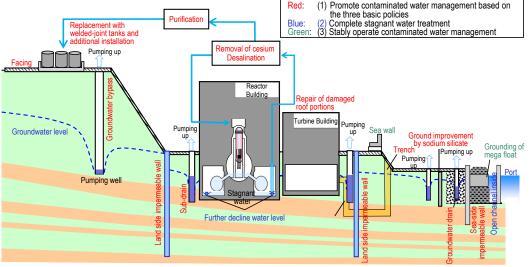

Progress status

- ◆ The temperatures of the Reactor Pressure Vessel (RPV) and Primary Containment Vessel (PCV) of Units 1-3 have been maintained within the range of approx. 15-20°C^{*1} over the past month. There was no significant change in the concentration of radioactive materials newly released from Reactor Buildings into the air*2. It was concluded that the comprehensive cold shutdown condition had been maintained.
- * 1 The values varied somewhat, depending on the unit and location of the thermometer.
- * 2 In February 2021, the radiation exposure dose due to the release of radioactive materials from the Unit 1-4 Reactor Buildings was evaluated at less than 0.00004 mSv/year at the site boundary. The annual radiation dose from natural radiation is approx. 2.1 mSv/year (average in Japan)

further insights collected

In response to Unit 1 and 3 PCV drops in

In response to the drops in water levels in the Unit 1

significant variation was detected, it was evaluated that

there was no immediate influence on nuclear safety.

Regarding Unit 1, the PCV water level had been

declining gradually. To monitor the PCV water level

stably, the reactor water injection rate was increased

and 3 Primary Containment Vessel (PCV), monitoring of plant parameters are enhanced at Unit 1-3. As no

water levels, monitoring enhanced and

Unit 3 Removal of all fuel assemblies from the Unit 3 spent fuel pool completed (February 28, 2021)

Removal of 566 fuel assemblies remaining in the Unit 3 spent fuel pool was completed. This is the first among the meltdown units.

As the top floor of the Unit 3 Reactor Building, where the spent fuel pool was located, was in a high-dose environment, rubble and fuel were removed by remote operation.

Despite various problems encountered during work, partner companies and TEPCO collaborated on an ongoing basis to improve matters and subsequently finished the planned work.

Lessons and insights acquired from this work will be utilized in fuel removal at Units 1 and 2.

Spent Fuel Pool

Operating floor

Water

iniectio

Reactor Building (R/B)

Windbreak

fence

Primary Dontainment

(PCV)

Pressure Vessel (RPV)

Fuel debris

Vessel (PCV)

2021/2 2013/10 2016/6 2016/12 2017/1 2017/11 2018/2 2019/4 Decontamination on the R/B top floor completed Removal of large rubble on the R/B top floor completed Shields installed on the R/B top floor Fuel-handling machine installed Installation of removal cover completed removal started Fuel removal completed nstallation of removal cover started Fuel



Front chamber

Blowout panel (closed)

Water

injectio



Removed fuel (assemblies)*1

(Fuel removal completed on February 28, 2021)

Water

injection

566/566



Dome roof

_Fuel-handling

machine Crane

FHM girder



Cover for fuel removal

Unit 4 * 2 Including two new fuel assemblie

Removed fuel (assemblies)

1535/1535*2

(Fuel removal completed on December 22, 2014)

on March 22 and an increase in water level was confirmed. Before investigating the PCV, further insights will be collected by checking the PCV water levels and others. <Fuel removal>

1568/1568

As part of efforts to clarify the progression of the accident, the insides of the Units 1-4 SGTS rooms were investigated

Toward clarifying the accident progression, the equipment and piping in the Units 1-4 Standby Gas Treatment System (SGTS) rooms were investigated sequentially.

The results of this investigation using a y-imager indicated contamination around/inside the SGTS filter trains of all Units, which is considered to be a result of backflow of vent gas. Also, accumulated water inside the SGTS filter trains was detected at Unit 3 and 4, which is considered to be condensed water of vent gas.

Efforts to clarify the accident progression will continue.

Operation of seismometers in Unit 3 resumed on March 19

Regarding seismometers, which were installed in the Unit 3 Reactor Building for trial operation, observation was suspended after they malfunctioned due to being immersed in rainwater and noise generation. Devel of 1F (Under the gentry on north-west side) Work is underway to investigate the West side (mountain side) cause of the noise.

Unit 1

These seismometers were replaced with new ones and trial operation resumed temporarily on March 19. Subsequently, the record of the Miyagi Prefecture Offshore Earthquake, which occurred the following day, was acquired.

By utilizing the acquired observation record, methods to identify the aging trend of the building and installation in Units 1 and 2 will continue to be examined.

2 Level of R/B roof (Under the cover on south-/East side (sea side) Unit 3 Reactor Building

<Location of seismometer installation>

Unit 2

Declining trend confirmed in the air dose rate and the surface contamination density on the Unit 2 Reactor Building top floor

Unit 3 *1 Fuel assemblies stored in

Before installing a fuel-handling facility in Unit 2, the air dose rate and surface contamination density were measured and an overall decline in these values of about 20% compared to the previous results (2018) was confirmed.

Measures to further reduce the dose rate will be prepared and work will continue.

To acquire further insights into decommissioning, the inside of the Unit 2 reactor well will be investigated.

Shooting location Result acquired in 2018 Result acquired in 2020


<Results acquired by the gamma camera>

Mid-and-Long-Term Decommissioning Action Plan 2021 revised

In March 2020, the "Mid-and-Long-Term Decommissioning Action Plan 2020" was published for indicating the main work processes involved in decommissioning as a whole, to achieve the goals laid out in the Mid-and-Long-Term Roadmap and the Nuclear Regulatory Authority (NRA) Risk Map.

Based on the progress of the decommissioning and challenges newly identified in FY2020, the plan was revised as the "Mid-and-Long-Term Decommissioning Action Plan 2021."

The initiatives undertaken during the decommissioning work are continuously unprecedented in the world. Accordingly, TEPCO will revise this plan regularly in accordance with the progress made and the challenges faced, as TEPCO systematically proceeds with safe and stable decommissioning.

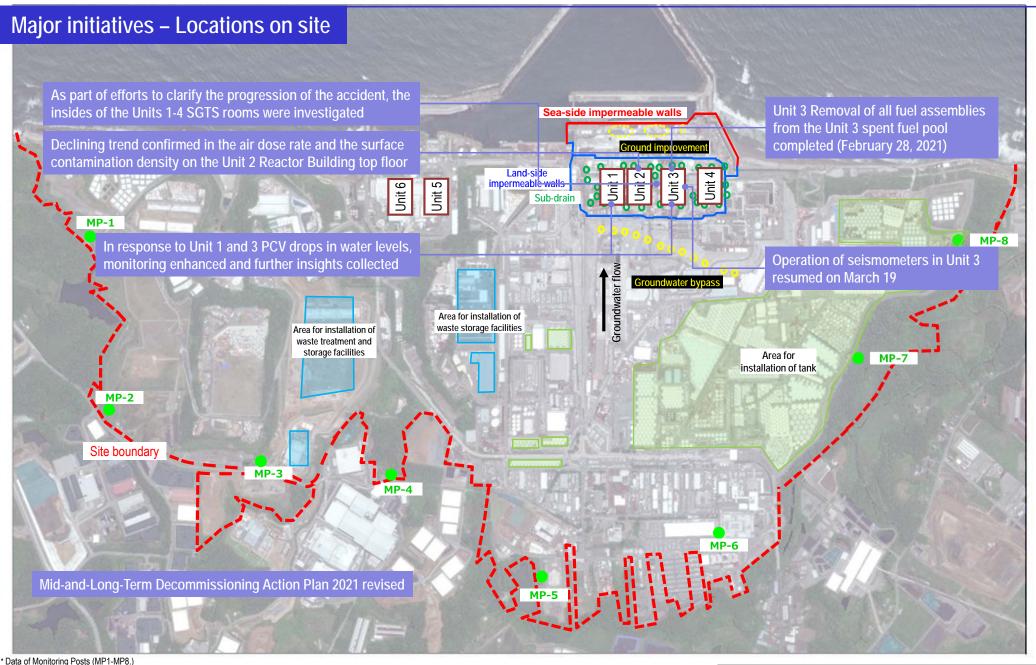

Data (10-minute values) of Monitoring Posts (MPs) measuring the airborne radiation rate around site boundaries showed 0.361 – 1.216 µSv/h (February 24 – March 23, 2021).

We improved the measurement conditions of monitoring posts 2 to 8 to measure the air-dose rate precisely. Construction work, such as tree-clearing, surface soil removal and shield wall setting, were implemented from February 10 to April 18, 2012.

Therefore, monitoring results at these points are lower than elsewhere in the power plant site.


The radiation shielding panels around monitoring post No. 6, which is one of the instruments used to measure the radiation dose at the power station site boundary, were taken off from July 10 - 11, 2013, since further deforestation, etc. had caused the surrounding radiation dose to decline significantly.


Provided by Japan Space Imaging Corp., photo taken on May 24, 2020 Product (C) [2020] DigitalGlobe, Inc., a Maxar company

I. Confirmation of the reactor conditions

1. Temperatures inside the reactors

Through continuous reactor cooling by water injection, the temperatures of the Reactor Pressure Vessel (RPV) bottom and the Primary Containment Vessel (PCV) gas phase were maintained within the range of approx. 15 to 20°C for the past month, though it varied depending on the unit and location of the thermometer.






- *1 The trend graphs show part of the temperature data measured at multiple points.
- *2 A part of data could not be measured due to maintenance and inspection of the facility and other work.

2. Release of radioactive materials from the Reactor Buildings

As of February 2021, the concentration of radioactive materials newly released from Reactor Building Units 1-4 into the air and measured at the site boundary was evaluated at approx. 1.7×10^{-12} Bg/cm³ and 2.0×10^{-12} Bg/cm³ for Cs-134 and -137 respectively, while the radiation exposure dose due to the release of radioactive materials there was less than 0.00004 mSv/vear.

Annual radiation dose at site boundaries by radioactive materials (cesium) released from Reactor Building Units 1-4



- The concentration limit of radioactive materials in the air outside the surrounding
- [Cs-134]: 2 x 10⁻⁵ Bq/cm^{3Marc}
- [Cs-137]: 3 x 10-5 Bq/cm3
- Data of Monitoring Posts (MP1-MP8)

Data of Monitoring Posts (MPs) measuring the air dose rate around the site boundary showed 0.361 – 1.216 µSv/h (February 24 – March 23, 2021).

To measure the variation in the air dose rate of MP2-MP8 more accurately, work to improve the environment (trimming trees, removing surface soil, and shielding around the MPs) was completed.

Note 1: Different formulas and coefficients were used to evaluate the radiation dose in the facility operation plan and monthly report. The evaluation methods were integrated in September 2012. As the fuel removal from the spent fuel pool (SFP) commenced for Unit 4, the radiation exposure dose from Unit 4 was added to the items subject to evaluation since November 2013. The evaluation has been changed to a method considering the values of continuous dust monitors since FY2015, with data to be evaluated monthly and announced the following month.

Note 2: Radiation dose was calculated using the evaluation values of release amount from Units 1-4 and Units 5 and 6. The radiation dose of Unit 5 and 6 was evaluated based on expected release amount during operation until September 2019 but the evaluation method was reviewed and changed to calculate based on the actual measurement results of Units 5 and 6 from October.

3. Other indices

There was no significant change in indices, including the pressure in the PCV and the PCV radioactivity density (Xe-135) for monitoring criticality, nor was any anomaly in the cold shutdown condition or criticality sign detected.

Based on the above, it was confirmed that the comprehensive cold shutdown condition had been maintained and the reactors remained in a stabilized condition.


II. Progress status by each plan

1. Contaminated water management

Based on the three basic policies: "remove" the source of water contamination, "redirect" fresh water from contaminated areas and "retain" contaminated water from leakage, multi-layered contaminated water management measures have been implemented to stably control groundwater

Status of contaminated water generated

- Multi-layered measures, including pumping up by sub-drains and land-side impermeable walls, which were implemented to control the continued generation of contaminated water, suppressed the groundwater inflow into buildings.
- After implementing "redirecting" measures (groundwater bypass, sub-drains, land-side impermeable walls and others) and rainwater prevention measures, including repairing damaged parts of building roofs, the amount of contaminated water generated within 2020 declined to approx. 140 m³/day.
- Measures will continue to further reduce the amount of contaminated water generated.

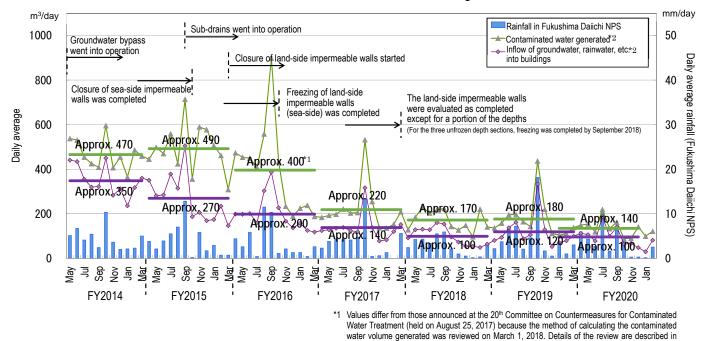

*2: The monthly daily average is derived from the daily average from the previous Thursday to the las Wednesday, which is calculated based on the data measured at 7:00 on every Thursday

Decommissioning and Contaminated Water Treatment.

the materials for the 50th and 51st meetings of the Secretariat of the Team for Countermeasures for

Figure 1: Changes in contaminated water generated and inflow of groundwater and rainwater into buildings

Operation of the groundwater bypass

- From April 9, 2014, the operation of 12 groundwater bypass pumping wells commenced sequentially to pump up groundwater. The release then started from May 21, 2014, in the presence of officials from the Intergovernmental Liaison Office for the Decommissioning and Contaminated Water Issue of the Cabinet Office. Up until March 23, 2021, 626,000 m³ of groundwater had been released. The pumped-up groundwater was temporarily stored in tanks and released after TEPCO and a third-party organization had confirmed that its quality met operational targets.
- Pumps are inspected and cleaned as required based on their operational status.

Operation of the Water-Treatment Facility special for Sub-drain & Groundwater drains

- To reduce the level of groundwater flowing into the buildings, work began to pump up groundwater from wells (subdrains) around the buildings on September 3, 2015. The pumped-up groundwater was then purified at dedicated facilities and released from September 14, 2015, in the presence of officials from the Intergovernmental Liaison Office for the Decommissioning and Contaminated Water Issue of the Cabinet Office. Up until March 22, 2021, a total of 1,052,000 m³ had been drained after TEPCO and a third-party organization had confirmed that its quality met operational targets.
- Due to the level of the groundwater drain pond rising after the sea-side impermeable walls had been closed, pumping started on November 5, 2015. Up until March 23, 2021, a total of approx. 259,000 m³ had been pumped up and a volume of under 10 m³/day is being transferred from the groundwater drain to the Turbine Buildings (average for the period February 18 – March 17, 2021).
- As one of the multi-layered contaminated-water management measures, in addition to a waterproof pavement that

- aims to prevent rainwater infiltrating, facilities to enhance the sub-drain treatment system were installed and went into operation from April 2018, increasing the treatment capacity from 900 to 1,500 m³/day and improving reliability. Operational efficiency was also improved to treat up to 2,000 m³/day for almost one week during the peak period.
- To maintain the groundwater level, work to install additional sub-drain pits and recover those existing is underway. The additional pits are scheduled to start operation sequentially, from pits for which work is completed (12 of 14 new sub-drain pits went into operation). To recover existing pits, work for all three pits scheduled was completed, all of which went into operation from December 26, 2018. Work to recover another pit (No. 49) started from November 2019 and it went into operation from October 9, 2020.
- To eliminate the need to suspend water pumping while cleaning the sub-drain transfer pipe, the pipe will be duplicated.
 Installation of the pipe and ancillary facilities was completed.
- Since the sub-drains went into operation, the inflow to buildings tended to decline to under 150 m³/day when the sub-drain water level declined below T.P. 3.0 m but increased during rainfall.




Figure 2: Correlation between inflow such as groundwater and rainwater into buildings and the water level of Units 1-4 sub-drains

> Implementation status of facing

- Facing is a measure involving asphalting of the on-site surface to reduce the radiation dose, prevent rainwater infiltrating the ground and decrease the amount of underground water flowing into buildings. As of the end of February 2021, 94% of the planned area (1,450,000 m² on site) had been completed. For the area inside the land-side impermeable walls, implementation proceeds appropriately after constructing a yard from implementable zones that do not affect the decommissioning work. As of the end of February 2021, 18% of the planned area (60,000 m²) had been completed.
- Construction status of the land-side impermeable walls and status of groundwater levels around the buildings
- An operation to maintain the land-side impermeable walls and prevent the frozen soil from thickening further continued from May 2017 on the north and south sides and started from November 2017 on the east side, where sufficiently thick frozen soil was identified. The scope of the maintenance operation was expanded in March 2018.
- In March 2018, construction of the land-side impermeable walls was completed, except for a portion of the depth, based on a monitoring result showing that the underground temperature had declined below 0°C in almost all areas, while on the mountain side, the difference in internal and external water levels increased to approx. 4-5 m. The 21st Committee on Countermeasures for Contaminated-Water Treatment, held on March 7, 2018, evaluated that alongside the function of sub-drains and other measures, a water-level management system to stably control groundwater and redirect groundwater from the buildings had been established and allowed the amount of contaminated water generated to be reduced significantly.
- A supplementary method was implemented for the unfrozen depth and it was confirmed that the temperature of this
 portion had declined below 0°C by September 2018. From February 2019, a maintenance operation started
 throughout all sections.

The groundwater level in the area inside the land-side impermeable walls has been declining every year. On the
mountain side, the difference between the inside and outside was maintained, despite varying during rainfall. The
water level of the groundwater drain observation well has been maintained at approx. T.P. +1.5 m, sufficiently below
the ground surface (T.P. 2.5 m).

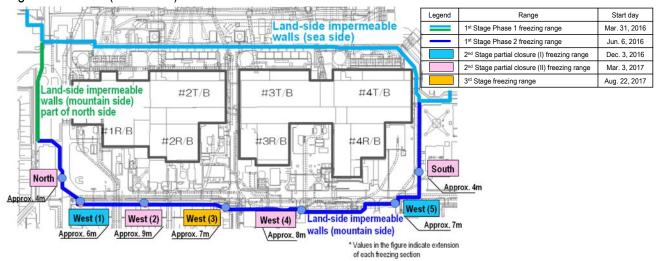


Figure 3: Closure parts of the land-side impermeable walls (on the mountain side)

Operation of multi-nuclide removal equipment

- Regarding the multi-nuclide removal equipment (existing and high-performance), hot tests using radioactive water are underway (for existing equipment, System A: from March 30, 2013, System B: from June 13, 2013, System C: from September 27, 2013; and for high-performance equipment, from October 18, 2014). The additional multi-nuclide removal equipment went into full-scale operation from October 16, 2017.
- As of March 18, 2021, the volumes treated by existing, additional and high-performance multi-nuclide removal equipment were approx. 463,000, 695,000 and 103,000 m³, respectively (including approx. 9,500 m³ stored in the J1(D) tank, which contained water with highly concentrated radioactive materials at the System B outlet of the existing multi-nuclide removal equipment).
- To reduce the risks of strontium-reduced water, treatment using existing, additional and high-performance multinuclide removal equipment has been underway (existing: from December 4, 2015; additional: from May 27, 2015; high-performance: from April 15, 2015). Up until March 18, 2021, approx. 783,000 m³ had been treated.


> Toward reducing the risk of contaminated water stored in tanks

 Treatment measures comprising the removal of strontium by cesium-absorption apparatus (KURION) (from January 6, 2015), the secondary cesium-absorption apparatus (SARRY) (from December 26, 2014) and the third cesiumabsorption apparatus (SARRY II) (from July 12, 2019) are underway. Up until March 18, 2021, approx. 629,000 m³ had been treated.

Measures in the Tank Area

Rainwater accumulates and is collected inside the area of contaminated-water tanks. After removing radionuclides, the rainwater is sprinkled over the site grounds, if the radioactivity level does not meet the standard for discharging into the environment since May 21, 2014 (as of March 22, 2021, a total of 175,000 m³).

As of March 18, 2021

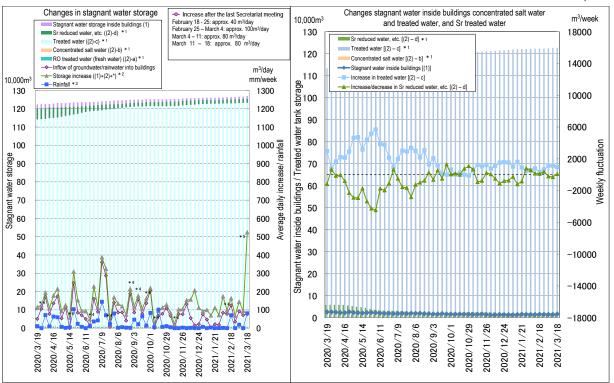

- *1: Water amount for which the water-level gauge indicates 0% or more
- *2: To detect storage increases more accurately, the calculation method was reviewed as follows from February 9, 2017: (The revised method was applied from March 1, 2018) [(Inflow of groundwater/rainwater into buildings) + (other transfer) + (chemical injection into ALPS)]
- *3: Changed from December 13, 2018 from rainfall in Namie to that within the site.
- *4: Considered attributable to the increased inflow of groundwater, rainwater, and others to buildings due to the decline in the level of stagnant water in buildings
- (March 18, May 7-14, June 11-18, July 16-23, August 20-27, September 3-10 and 17-24, October 1-8, November 12-19, 2020 and February 4-11,2021)
- *5. Stored amount increased due to transfer to buildings in association with decommissioning work on March 18, 2021.

 (Major breakdown of the transferred amount: (1) Stagnant water inside the tank fences (water transferred from the Shallow Draft Quay drainage channel) was transferred to the Process Main Building: approx. 390 m³/day, (2) Stagnant water inside the tank fences (water transferred from the Shallow Draft Quay drainage channel) was transferred to the High Temperature Incinerator Building: approx. 10 m³/day, (3) Transfer from the Unit 3 additional FSTR to the Unit 3 Radioactive Waste Treatment Building: approx. 10 m³/day and others)

Figure 4: Status of stagnant water storage

Progress status of stagnant water in buildings and others

- TEPCO aims to reduce the amount of stagnant water in the Unit 1-3 R/Bs, where circulation water injection is conducted, to about half of the amount at the end of 2020 during the period FY2022-2024.
- At present, based on the influence on succeeding-stage facilities of the rapid concentration change after treating highly concentrated stagnant water containing dust and α-nuclide existing in the lower part of the R/Bs, the water level is being reduced carefully.

2. Fuel removal from the spent fuel pools

Work to help remove spent fuel from the pool is progressing steadily while ensuring seismic capacity and safety.

Main work to help spent fuel removal at Unit 1

- After examining two methods: (i) installing a cover after rubble removal and (ii) initially installing a large cover over the Reactor Building and then removing rubble inside the cover, method (ii) was selected to ensure safer and more secure removal.
- Before removing the fallen roof and other objects on the south side, to minimize the risk of the overhead crane/fuel-handling machine shifting its position, becoming imbalanced and subsequently falling, materials to support the fuel-handling machine from below will be installed.
- Among the measures to prevent and alleviate rubble falling, work to install supports for the Unit 1 fuel-handling machine started from October 6, 2020 and was completed by October 23.
- To install the support for the overhead crane, preparation started from October 2020 and the work was completed on November 24.
- From December 19, 2020, before installing a large cover over the Unit 1 Reactor Building, dismantling of the interfering building cover (remaining part) started. The dismantling will be completed in June 2021 and work to install a large

cover will start from the first half of FY2021.

 Rubble removal and other work will proceed steadily with safety first, toward starting fuel removal during the period FY2027 to FY2028.

Main work to help spent fuel removal at Unit 2

- After completing the training to practice work skills for transportation, preparatory work inside the operating floor started from July 20, 2020. Containers housing the remaining objects during the previous work were transported to the solid waste storage facility from August 26, which was completed by December 11.
- For fuel removal methods, based on the investigative results inside the operating floor from November 2018 to February 2019, a method to access from a small opening installed on the south side of the building was selected with aspects such as dust management and lower work exposure in mind (the method previously examined had involved fully dismantling the upper part of the building).

Completion of fuel removal at Unit 3

- On October 11, 2013, removal of large rubble on the top floor of the Reactor Building was completed.
- On November 21, 2015, removal of large rubble inside the spent fuel pool using a crawler crane was completed.
- On June 10, 2016, decontamination on the top floor of the Reactor Building was completed. On December 2, installation of shielding on the top floor of the Reactor Building was completed.
- On January 17, 2017, installation of a cover for fuel removal started. On November 12, a fuel-handling machine was installed inside the cover.
- On February 23, 2018, installation of a cover for fuel removal was completed.
- · On April 15, 2019, fuel removal started.
- On February 28, 2021, fuel removal was completed.

3. Retrieval of fuel debris

Response to high concentration contamination of the Unit 2 shield plug

- To check the inside of the reactor well under the Unit 2 shield plug, an investigation using the reactor cavity differential pressure control line is planned.
- Three on-site investigations were already conducted to measure the radiation dose and identify the on-site conditions, including the surrounding area.
- The investigative result confirmed that the valve to be installed in the reactor cavity differential pressure control line was open and only the straight line to the exhaust duct was degraded. It also detected high-dose points under the duct and near the floor surface at four meters below the duct.
- After acquiring detailed radiation data, shielding and others will be installed. Based on the on-site dose after the shielding is installed and the contamination condition there, a detailed work plan will be formulated.

4. Plans to store, process and dispose of solid waste and decommission of reactor facilities

Promoting efforts to reduce and store waste generated appropriately and R&D to facilitate adequate and safe storage, processing and disposal of radioactive waste

Management status of the rubble and trimmed trees

- As of the end of February 2021, the total storage volume for concrete and metal rubble was approx. 309,900 m³ (+300 m³ compared to at the end of January with an area-occupation rate of 76%). The total storage volume of trimmed trees was approx. 134,400 m³ (slight increase, with an area-occupation rate of 77%). The total storage volume of used protective clothing was approx. 31,200 m³ (+900 m³, with an area-occupation rate of 46%). The increase in rubble was mainly attributable to work around the Unit 1-4 buildings, transfer for area arrangement, decontamination work of flanged tanks, work related to water-treatment facilities and work around the Unit 5 and 6 buildings, while the increase in used protective clothing was attributable to the suspension of incinerator operation.
- Management status of secondary waste from water treatment
- As of March 4, 2021, the total storage volume of waste sludge was 421 m³ (area-occupation rate: 60%), while that of concentrated waste fluid was 9,322 m³ (area-occupation rate: 91%). The total number of stored spent vessels, High-


Integrity Containers (HICs) for multi-nuclide removal equipment and other vessels, was 5,056 (area-occupation rate: 79%).

- Progress status of the additional Radioactive Waste Incinerator in the Fukushima Daiichi Nuclear Power Station
- During the system test for the additional Radioactive Waste Incinerator (inside inspection of the reactor after dry-fired operation), wear exceeding expectations was detected in the rotating section sliding material of the rotary kiln seal parts (on the inlet and outlet sides).
- Based on the on-site investigation results, this event was considered attributable to the following two causes:
- 1. Axial runout of the rotary kiln causing the sliding surface to hit locally and accelerated the wear of the sliding material
- 2. The step of the sliding surface mating section on the fixed side causing the wear of the sliding surface on the rotating side to intensify.
- · Based on these two causes, the structure of the rotary kiln seal parts will be modified.
- For this modification, the completion of the additional Radioactive Waste Incinerator will be revised to March 2022.


5. Reduction in radiation dose and mitigation of contamination

Effective dose-reduction at site boundaries and purification of port water to mitigate the impact of radiation on the external environment

- > Status of groundwater and seawater on the east side of Turbine Building Units 1-4
- In the Unit 1 intake north side area, the H-3 concentration was below the legal discharge limit of 60,000 Bq/L at all observation holes and remained constant or has been declining overall. The concentration of total-β radioactive materials increased temporarily from April 2020 but currently remains constant or is declining overall.
- In the area between the Unit 1 and 2 intakes, the H-3 concentration has remained below the legal discharge limit of 60,000 Bq/L at all observation holes. It has been increasing or decreasing at No. 1-14 but has remained constant or been declining at many observation holes overall. The concentration of total-β radioactive materials has remained constant or been declining at many observation holes overall.
- In the area between the Unit 2 and 3 intakes, the H-3 concentration has been below the legal discharge limit of 60,000 Bq/L at all observation holes and remained almost constant or been declining, although increasing at No. 2-5. The concentration of total-β radioactive materials has remained almost constant or been declining overall though increasing at No. 2-5.
- In the area between the Unit 3 and 4 intakes, the H-3 concentration has been below the legal discharge limit of 60,000 Bq/L at all observation holes and remained constant or been declining. The concentration of total-β radioactive materials has also remained constant or been declining overall.
- The concentration of radioactive materials in drainage channels has remained constant, despite increasing during rainfall.
- In the Units 1-4 open channel area of seawater intake for Units 1 to 4, the concentration of radionuclides in seawater has remained below the legal discharge limit, despite increases in Cs-137 and Sr-90 noted during rainfall. They have also been declining following the completed installation and the connection of steel pipe sheet piles for the sea-side impermeable walls. The concentration of Cs-137 has remained slightly higher in front of the south side impermeable walls and slightly lower on the north side of the east breakwater since March 20, 2019, when the silt fence was transferred to the center of the open channel due to mega float-related construction.
- In the port area, the concentration of radionuclides in seawater has remained below the legal discharge limit, despite increases in Cs-137 and Sr-90 observed during rainfall. They have remained below the level of those in the Units 1-4 intake open channel area and been declining following the completed installation and connection of steel pipe sheet piles for the sea-side impermeable walls.
- In the area outside the port, regarding the concentration of radioactive materials in seawater, those of Cs-137 and Sr-90 declined and remained low after steel pipe sheet piles for the sea-side impermeable walls were installed and connected.

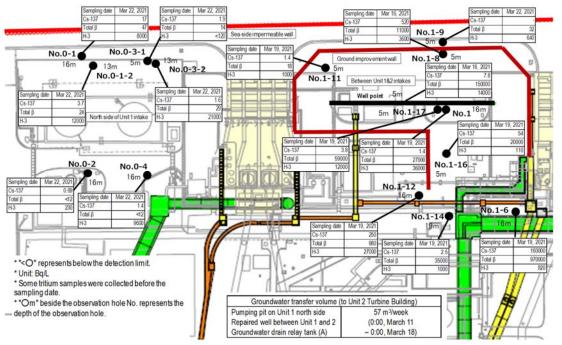

<Unit 1 intake north side, between Unit 1 and 2 intakes>

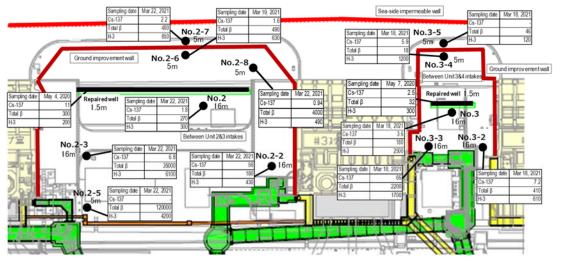

<Between Unit 2 and 3 intakes, between Unit 3 and 4 intakes>

Figure 5: Groundwater concentration on the Turbine Building east side

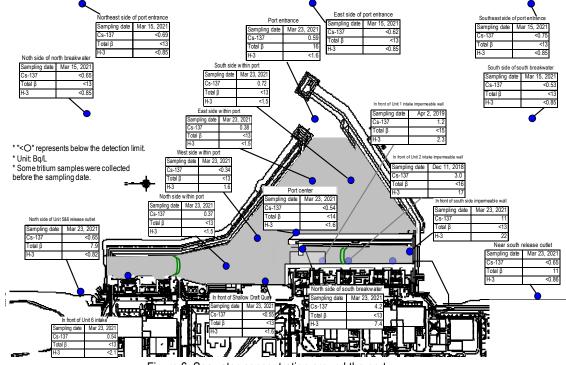


Figure 6: Seawater concentration around the port

- High-radioactivity alarm issued by the simple radiation detector (PSF monitor) of the Shallow Draft Quay drainage channel
- On March 2, a high alarm (value: 1,500Bq/L) was issued by the PSF(Plastic Scintillation Fiber) monitor installed at the Shallow Draft Quay drainage channel.
- No significant variation was detected in the monitoring posts, boundary dust monitors and on-site continuous dust monitors. No abnormality was identified in the plant parameters of Unit 1-4 and water treatment facilities.
- On the same day, the sea water of the Shallow Draft Quay drainage channel was sampled. As an increase in total β radioactivity was confirmed, the electric gate of the drainage channel was closed and drainage transfer from the Shallow Draft Quay drainage channel to the inner fence area of K2 tank started.
- As the analysis of water sampled from the Shallow Draft Quay drainage channel confirmed that the RADIOACTIVE CONCENTRATION WAS within the normal range and cleaning of the Shallow Draft Quay drainage channel was completed, the gate installed at the Shallow Draft Quay drainage channel was opened on March 9.
- As an investigation conducted during rainfall on March 13 could not identify the inflow source, an additional investigation was implemented for the period March 21-22, including intensive measurement on the branch pipes to the drainage channel. The PSF monitor data was reanalyzed and the result confirmed a high total-β concentration in drainage from the temporary storage area W.
- The contamination source was considered to be located in the temporary storage area W and an on-site investigation detected a gel mass with β contamination. The contamination source in the temporary storage area W was removed and the location confirmed as β-contaminated was covered by a sheet.
- The surface will be stripped, while investigations into the cause and monitoring of the radioactivity in the drainage channel continue.

6. Outlook of the number of staff required and efforts to improve the labor environment and conditions

Adequate number of staff will be secured in the long-term, while firmly implementing radiation control of workers. The work environment and labor conditions will be continuously improved by responding to the needs on the site.

> Staff management

- The monthly average total of personnel registered for at least one day per month to work on site during the past quarter from November 2020 to January 2021 was approx. 8,900 (cooperating company workers and TEPCO HD employees), which exceeded the monthly average number of actual workers (approx. 6,700). Accordingly, sufficient personnel are registered to work on site.
- It was confirmed with the prime contractors that the estimated manpower necessary for the work in March 2021 (approx. 3,500 weekday per day: cooperating company workers and TEPCO HD employees) would be secured at present. The average numbers of workers per day for each month (actual values) of recent 2 years were maintained, with approx. 3,400 to 4,200 (see Figure 7).
- The number of workers from within Fukushima Prefecture remained constant while those from outside increased. The local employment ratio (cooperating company workers and TEPCO HD employees) as of February 2021 also remained constant at around 65%.
- The monthly average exposure doses of workers remained at approx. 0.22, 0.20 and 0.21 mSv/month during FY2017, 2018 and 2019, respectively. (Reference: Annual average exposure dose 20 mSv/year ≒ 1.7 mSv/month)
- For most workers, the exposure dose was sufficiently within the limit and allowed them to continue engaging in radiation work.




Figure 7: Changes in the average number of workers weekday per day for each month of recent 2 years (actual values)

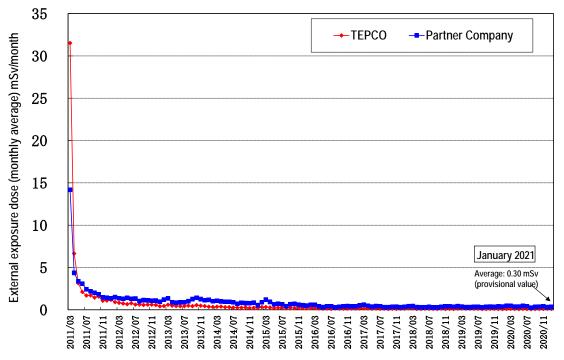


Figure 8: Changes in monthly individual worker exposure dose (monthly average exposure dose since March 2011)

➤ Measures to prevent infection and expansion of influenza and norovirus

• Since November, measures for influenza and norovirus have been implemented, including free influenza vaccinations (subsidized by TEPCO HD) at medical clinics around the site (from October 12, 2020 to January 28, 2021) for partner company workers. As of January 28, 2021, a total of 5,393 had been vaccinated. In addition, other measures are also being implemented across the board, including daily actions to prevent infection and expansion (measuring body temperature, health checks and monitoring infection status) and response after detecting possible infections (swift exit of possible patients and control of entry, mandatory wearing of masks in working spaces, etc.).

Status of influenza and norovirus cases

• Until the 11st week of 2021 (March 15-21, 2021), one influenza infection and one norovirus infection respectively were recorded. The totals for the same period for the previous season showed 169 cases of influenza and ten norovirus infections.

Note: The above data is based on reports from TEPCO and partner companies, which include diagnoses at medical clinics outside the site.

The subjects of this report were workers of partner companies and TEPCO in Fukushima Daiichi and Daini Nuclear Power Stations.

COVID-19 infectious disease countermeasures

 As of 15:00, March 24, 2021, 11 TEPCO HD employees and cooperating company workers (including one TEPCO HD employee) of the Fukushima Daiichi Nuclear Power Station (NPS) had contracted COVID-19. No significant influence on decommissioning work, such as a delay to the work processes due to this infection, had been identified. Countermeasures have continued to prevent the COVID-19 infection spreading, such as requiring employees to take
their temperature prior to coming to the office, wear masks at all times and avoid the "Three Cs" (Closed spaces,
Crowded places, Close-contact settings) by using the rest house in shifts and others, eating silently, etc.

7. Status of Units 5 and 6

- Status of spent fuel storage in Units 5 and 6
- Regarding Unit 5, fuel removal from the reactor was completed in June 2015. A total of 1,374 spent and 168 non-irradiated fuel assemblies, respectively, were stored in the spent fuel pool (storage capacity: 1,590 assemblies).
- Regarding Unit 6, fuel removal from the reactor was completed in November 2013. A total of 1,456 spent and 198 non-irradiated fuel assemblies (180 of which transferred from the Unit 4 spent fuel pool) are stored in the spent fuel pool (storage capacity: 1,654), while 230 non-irradiated fuel assemblies are stored in the storage facility of non-irradiated fuel assemblies (storage capacity: 230).
- Status of stagnant water treatment in Units 5 and 6
- Stagnant water in Units 5 and 6 is transferred from Unit 6 Turbine Building to the outdoor tanks and sprinkled after undergoing oil separation and RO treatment and confirming the concentration of the radioactive materials.

8. Other

- ➤ Influence on tanks by the earthquake on February 13
- An investigation (involving inspection of leakage, sliding and connection pipes) into the influence of the earthquake at 23:08 on February 13 was conducted for tanks (a total of 1,837) within the Fukushima Daiichi Nuclear Power Station.
- For all mid- and low-concentration tanks (1,074), no leakage was detected and for 53 of them, tank sliding was identified.
- For these sliding tanks (53), the connection pipes are being inspected.
- Among the other tanks (763), leakage was detected from two tanks in F area which stored Unit 5 and 6 stagnant water (low-level). After reducing the water level to the leakage location or low, leakage has now ceased and the operation of these two tanks was suspended.
- Detailed inspections will be planned and implemented.
- ➤ Body contamination at the Process Main Building
 - On March 10, a post-work contamination inspection at the Unit 1-4 entry control facility of a TEPCO HD employee, who had checked lines of transfer pipes at the Process Main Building on site, confirmed that radioactive materials had adhered to his face, neck, body, arms and legs.
- As a nasal smear at the access control facility detected contamination, the possibility of internal uptake of radioactive materials was considered.
- On March 11, after removing residual contamination on the body surface, measurement by a whole-body counter was conducted. The calculation result confirmed that the deposited effective dose was below the recording level (2mSv).
 Moreover, on same day, an interview diagnosis by an ER doctor confirmed no abnormality.
- As an emergency measure, a rule was stipulated to assign multiple workers for areas where a safe work environment
 was not secured, such as high-dose or highly contaminated areas, or dark places. In addition, installation of lights at
 the Process Main Building will be planned.



Status of seawater monitoring within the port (comparison between the highest values in 2013 and the latest values)

"The highest value" → "the latest value (sampled during March 15-22)"; unit (Bq/L); ND represents a value below the detection limit

Summary of TEPCO data as of March 23, 2021

Note: The Total β measurement values include natural potassium 40 (approx. 12 Bq/L). They also include the contribution of yttrium 90, which radioactively balance stront

: 60 $(H25/8/19) \rightarrow ND(1.5)$ Below 1/40

ND(0.53)

ND(0.53)

Summary o	f TEP	CO data as of	Maı	rch 23, 202	21							The	y also in
						Cesium-134	ND(0.41)	1				Cesium-134	1 : 3.3
						Cesium-137	ND(0.54)					Cesium-137	7 : 7.3
						Total β	ND(13)					Total β	: 69
						Toritium	ND(1.6)	*1				Toritium	: 68
								l -					
Cesium-134	: 3.	3 (H25/10/17)	\rightarrow	ND(0.35)	Below 1/9	1							Cesium
Cesium-137	: 9	(H25/10/17)	\rightarrow	0.67	Below 1/10								Cesium
Total β	: 74	(H25/8/19)	\rightarrow	ND(14)	Below 1/5						X		Total β
Toritium	: 67	(H25/8/19)	\rightarrow	ND(1.5)	Below 1/40				[Dort	antrona 1			Toritiun
						'			L Po⊓	entrance]			-
Cesium-134	: 4.	4 (H25/12/24)	\rightarrow	ND(0.32)	Below 1/10						W/	•/	
Cesium-137	: 10	(H25/12/24)	\rightarrow	0.66	Below 1/10					1.20		N.	
Total β	: 60	(H25/7/4)	\rightarrow	ND(14)	Below 1/4								
Toritium	: 59	(H25/8/19)	\rightarrow	1.6	Below 1/30				1			WI III	
							. \				ď		
Cesium-134	: 5	(H25/12/2)	\rightarrow	ND(0.25)	Below 1/20		\ '		[East sid	de in the port	[South side in the	port]	
Cesium-137	: 8.	4 (H25/12/2)	\rightarrow	0.35	Below 1/20								
Total β	: 69	(H25/8/19)	\rightarrow	ND(14)	Below 1/4					[Port cen		4///	
Toritium	: 52	(H25/8/19)	\rightarrow	ND(1.5)	Below 1/30					L Port cen	ter	M	77
						[Nor	h side in the po	ort] [West sid			11		₩ *
					(In front	of Unit 6 intake	T	F (In front	of shallow quay]	. °	*4 (() *2	ु्रुपा	*2
)))	dran	quay 1	n solid	1-2-7-11-E-J		*3
) DC	CCC			*4
							4 Ploo(O)		80		gran longs		
	Seas	ide impermeable wall				0.00	6 3 444	**************************************	1		ما المصدوقة		≖ 3
	C:IF E	Silt fence					(M)		-8	号機	12号機 1号	機 4号機	ΠŽ
	SIIT	ence for construction				幾 5号機			/1/10		TH an dh	1200	med D
L					∖≒िका	h/1.	n 616	ril /	177				~ }}
						ika i · K	11112000	LI LI 1///	1 17/11/	7			
Cesium-134	: 2.	8 (H25/12/2)	-	ND(0.51)	Below 1/5	1		Cesium-134	: 5.3	(H25/8/5)	→ ND(0.55)	Below 1/	9
Cesium-137	: 5.	8 (H25/12/2)	_	ND(0.49)	Below 1/10			Cesium-137	: 8.6	(H25/8/5)	− 0.76	Below 1/1	0
Total β	: 46	(H25/8/19)	\rightarrow	15	Below 1/3			Total β	: 40	(H25/7/3)	→ 14	Below 1/2	2 Source
Toritium	: 24	(H25/8/19)	_	ND(2.1)	Below 1/10			Toritium	: 340	(H25/6/26)	- ND(1.6)	Below 1/20	0

Toritium	: 68 (H25	/8/19)	→ ND(1.6	5)	Below 1/40	
	Cesium-134	: 3.5	(H25/10/17)	\rightarrow	ND(0.27)	Below 1/10
	Cesium-137	: 7.8	(H25/10/17)	\rightarrow	0.39	Below 1/20
	Total B	: 79	(H25/8/19)	\rightarrow	ND(14)	Below 1/5

(H25/12/24) →

(H25/10/11) →

(H25/8/19) →

Cesium-134	:	32	(H25/10/11)	\rightarrow	ND(0.69)	Below 1/40	ı
Cesium-137	:	73	(H25/10/11)	\rightarrow	3.7	Below 1/10	ı
Total $oldsymbol{eta}$:	320	(H25/8/12)	\rightarrow	14	Below 1/20	ı
Toritium	:	510	(H25/9/2)	\rightarrow	7.4	Below 1/60	ı

Below 1/6

Below 1/5

Below 1/10

	Cesium-134	0.88
	Cesium-137	18
1	Total $oldsymbol{eta}$	31
	Toritium	22

- *1: Monitoring commenced in or after March 2014. Monitoring inside the sea-side impermeable walls was finished because of the landfill.
- *2: For the point, monitoring was finished from December 12, 2018 due to preparatory work for transfer of mega fl
- *3: For the point, monitoring point was moved from February 6, 2019 due to preparatory work for transfer of mega
- *4: For the point, monitoring was finished from April 3, 2019 due to preparatory work for transfer of mega float.

	Legal discharge limit	WHO Guidelines for Drinking Water Quality
Cesium-134	60	10
Cesium-137	90	10
Strontium-90 (strongly correlate with Total β)	30	10
Tritium	60,000	10,000

urce: TEPCO website Analysis results on nuclides of radioactive materials around Fukushima Daiichi

Nuclear Power Station http://www.tepco.co.jp/decommision/planaction/monitoring/index-j.html

Status of seawater monitoring around outside of the port (comparison between the highest values in 2013 and the latest values)

Unit (Bg/L); ND represents a value below the detection limit; values in () represent the detection limit; ND (2013) represents ND throughout 2013

(The latest values sampled during March 15-22)

	Legal discharge limit	Guidelines fo Drinking Water Quality
Cesium-134	60	10
Cesium-137	90	10
Strontium-90 (strongly correlate with Total β)	30	10
Tritium	60.000	10.000

ND(0.85)

ND(0.75)

ND(13)

ND(0.85)

ND(0.76)

ND(0.53)


ND(13)

ND(0.85)

Summary of TEPCO data as of March 23, 2021

Silt fence

Silt fence for construction

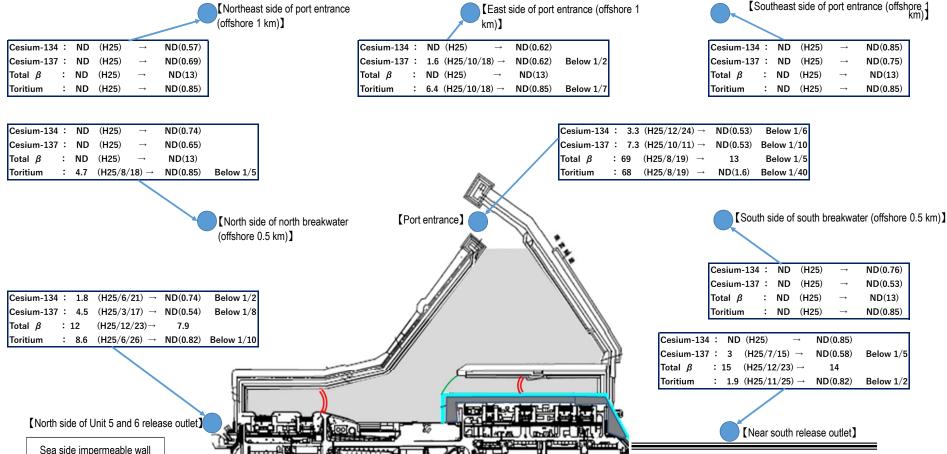


Note: The Total β measurement values include natural potassium 40 (approx. 12 Bq/L).

They also include the contribution of yttrium 90, which radioactively balance strontium 90.

Note: Because safety of the sampling points was unassured due to the influence of Typhoon No. 10 in 2016, samples were taken from approx. 330 m south of the Unit 1-4 release outlet.

Samples were also taken from a point approx. 280m south from the same release

outlet from January 27, 2017 and approx. 320m from March 23, 2018. Source: TEPCO website, Analysis results on nuclides of radioactive materials around Fukushima Daiichi Nuclear Power Station http://www.tepco.co.jp/decommision/planaction/monitoring/index-j.html

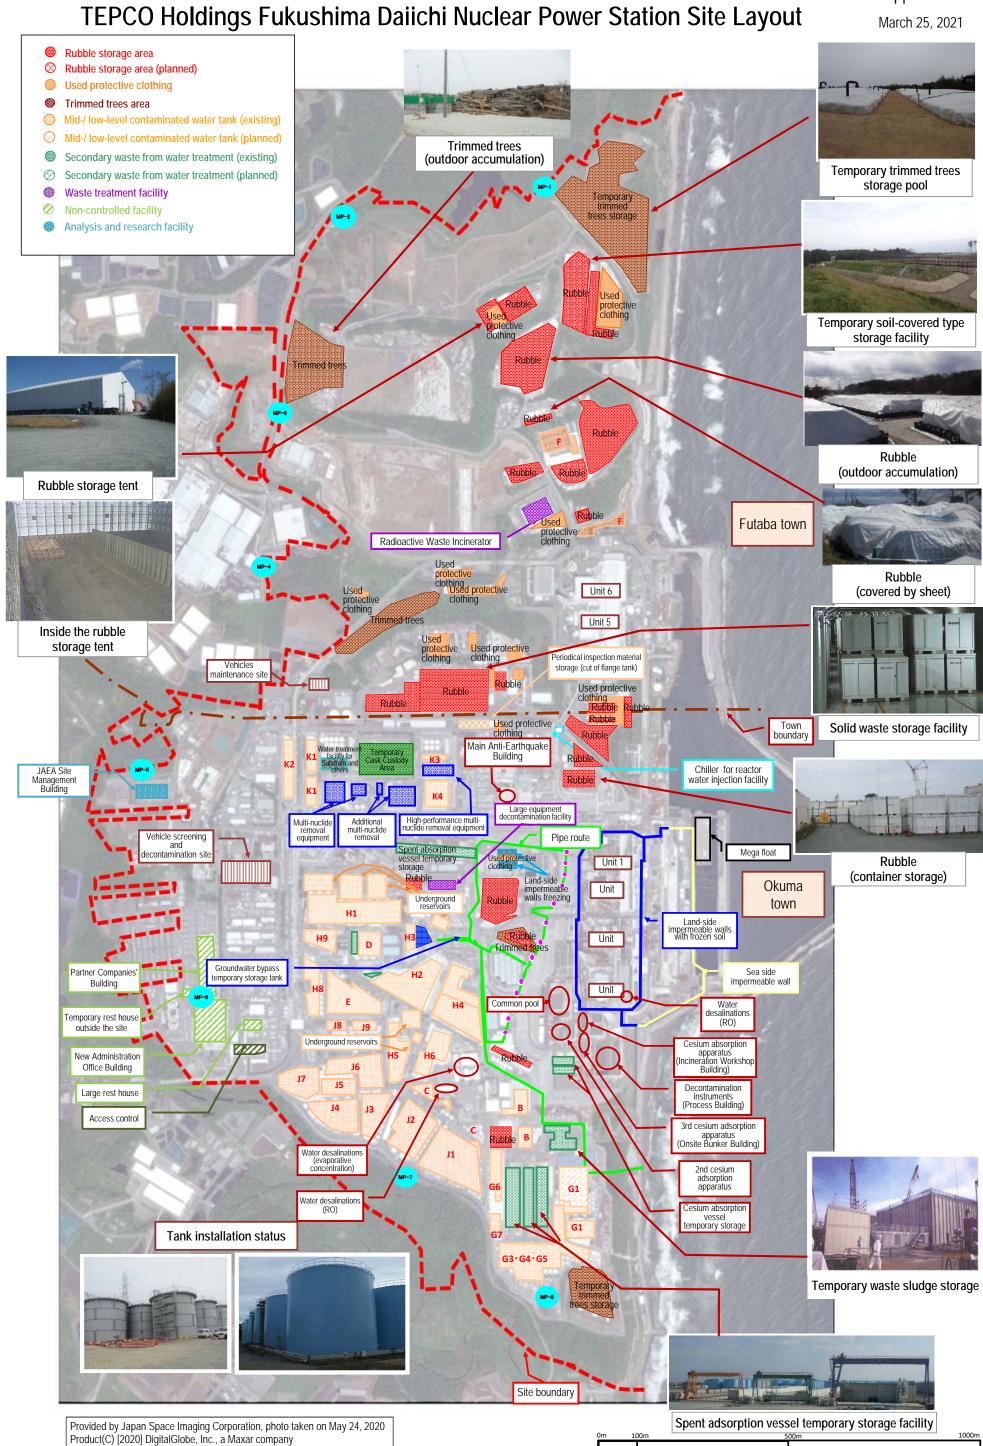

Progress toward decommissioning: Fuel removal from the spent fuel pool (SFP)

Immediate target

Commence fuel removal from the Unit 1-2 Spent Fuel Pools

March 25, 2021

Secretariat of the Team for Countermeasures for Decommissioning and Contaminated Water Treatment

1/6

Unit 1

Toward fuel removal from the Unit 1 spent fuel pool, investigations have been implemented to ascertain the conditions of the fallen roof on the south side and the contamination of the well plug. Based on the results of these investigations, "the method to initially install a large cover over the Reactor Building and then remove rubble inside the cover" was selected to ensure a safer and more secure removal. Work to install a large cover will start from the first half of FY2021. Work continues to complete installation of a large cover by around FY2023 and start fuel removal from FY2027 to FY2028.

<Reference> Progress to date

Rubble removal on the north side of the operating floor started from January 2018 and has been implemented sequentially. In July and August 2019, the well plug, which was misaligned from its normal position, was investigated and in August and September, the conditions of the overhead crane were checked. Based on the results of these investigations as the removal requires more careful work taking dust scattering into consideration, two methods were examined: installing a cover after rubble removal and initially installing a large cover over the Reactor Building and then removing rubble inside the cover.




Fuel-handing to

moval (image) Fuel removal

Unit 2

Toward fuel removal from the Unit 2 spent fuel pool, based on findings from internal operating floor investigations from November 2018 to February 2019, instead of fully dismantling the upper part of the building, the decision was made to install a small opening on the south side and use a boom crane. Examination continues to start fuel removal from FY2024 to FY2026.

<Reference> Progress to date
Previously, potential to recover the existing
overhead crane and the fuel handling
machine was examined. However, the high
radiation dose inside the operating floor
meant the decision was taken to dismantle
the upper part of the building in November
2015. Findings from internal investigations of
the operating floor from November 2018 to
February 2019 underlined the potential to
conduct limited work there and the means of
accessing from the south side had been
examined.




Overview of fuel removal (bird's-eye view)

Unit 3

Prior to the installation of a cover for fuel removal, removal of large rubble from the spent fuel pool was completed in November 2015. To ensure safe and steady fuel removal, training of remote control was conducted at the factory using the actual fuel-handling machine which will be installed on site (February – December 2015). Measures to reduce dose on the Reactor Building top floor (decontamination, shields) were completed in December 2016. Installation of a cover for fuel removal and a fuel-handling machine is underway from January 2017. Installation of the fuel removal cover was completed on February 23, 2018.

Toward fuel removal, the rubble retrieval training inside the pool, which was scheduled in conjunction with fuel removal training, started from March 15, 2019, and started fuel removal from April 15, 2019. Fuel removal was completed on February 28, 2021.







uel removal (566th assemb (February 26, 2021)

Unit 4

In the Mid- and-Long-Term Roadmap, the target of Phase 1 involved commencing fuel removal from inside the spent fuel pool (SFP) of the 1st Unit within two years of completion of Step 2 (by December 2013). On November 18, 2013, fuel removal from Unit 4, or the 1st Unit, commenced and Phase 2 of the roadmap started.

On November 5, 2014, within a year of commencing work to fuel removal, all 1,331 spent fuel assemblies in the pool had been transferred. The transfer of the




Fuel removal status

remaining non-irradiated fuel assemblies to the Unit 6 SFP was completed in December 22, 2014. (2 of the non-irradiated fuel assemblies were removed in advance in July 2012 for fuel checks)

This marks the completion of fuel removal from the Unit 4 Reactor Building. Based on this experience, fuel assemblies will be removed from other Unit pools.


* A part of the photo is corrected because it includes sensitive information related to physical protection.

Common pool



An open space will be maintained in the common pool (Transfer to the temporary cask custody area) Progress to date

- The common pool has been restored to a condition allowing it to re-accommodate fuel to be handled (November 2012)
- Loading of spent fuel stored in the common pool to dry casks commenced (June 2013)
- Fuel removal from the Unit 4 spent fuel pool began to be received (November 2013 - November 2014)
- Fuel removal from the Unit 3 spent fuel pool began to be received (April 2019 February 2021)



Operation commenced on April 12, 2013; from the cask-storage building, transfer of 9 existing dry casks completed (May 21, 2013); fuel stored in the common pool sequentially transferred.

<Glossa

- (*1) Operating floor: During regular inspection, the roof over the reactor is opened while on the operating floor, fuel inside the core is replaced and the core internals are inspected.
- (*2) Cask: Transportation container for samples and equipment, including radioactive materials.

Immediate target

Identify the plant status and commence R&D and decontamination toward fuel debris retrieval

Secretariat of the Team for Countermeasures for Decommissioning and Contaminated Water Treatment


Investigation into TIP Room of the Unit 1 Reactor Building

- To improve the environment for future investigations inside the PCV, etc., an investigation was conducted from September 24 to October 2, 2015 at the TIP Room(*1). (Due to high dose around the entrance in to the TIP Room, the investigation of dose rate and contamination distribution was conducted through a hole drilled from the walkway of the Turbine Building, where the dose was low)
- The investigative results identified high dose at X-31 to 33 penetrations^(*2) (instrumentation penetration) and low dose at
- As it was confirmed that work inside the TIP room would be available, the next step will include identification of obstacles which will interfere the work inside the TIP Room and formulation of a plan for dose reduction

Investigation in the leak point detected in the upper part of the Unit 1 Suppression Chamber (S/C(*3))

Investigation in the leak point detected in the upper part of Unit 1 S/C from May 27, 2014 from one expansion joint cover among the lines installed there. As no leakage was identified from other parts, specific methods will be examined to halt the flow of water and repair the PCV.






Leak point

Image of the S/C upper part investigation

Unit 1

Air dose rate inside the Reactor Building: Max. 5,150mSv/h (1F southeast area) (measured on July 4, 2012)

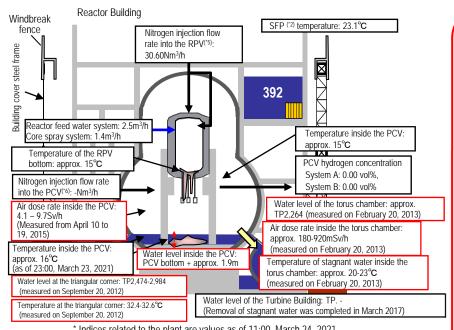


indices related to the plant are values as of 11.00, March 24, 2021						
Investigations inside PCV	1st (Oct 2012)	- Acquiring images - Measuring air temperature and dose rate - Measuring water level and temperature - Sampling stagnant water - Installing permanent monitoring instrumentation				
	2nd (Apr 2015)	Confirming the status of PCV 1st floor - Acquiring images - Measuring air temperature and dose rate - Replacing permanent monitoring instrumentation				
made i ov	3 rd (Mar 2017)	Confirming the status of PCV 1st basement floor - Acquiring images - Measuring and dose rate - Sampling deposit - Replacing permanent monitoring instrumentation				
Leakage points from PCV	PCV vent pipe vacuum break line bellows (identified in May 2014) - Sand cushion drain line (identified in November 2013)					

Status of investigation inside the PCV

Prior to fuel debris retrieval, an investigation inside the PCV will be conducted to inspect the status there including the location of fuel debris.

[Investigative outline]

- In April 2015, a device, which entered the inside of the PCV through a narrow access opening (bore: φ 100 mm), collected information such as images and airborne dose inside the PCV 1st floor.
- In March 2017, the investigation using a self-propelled investigation device, conducted to inspect the spreading of debris to the basement floor outside the pedestal, took images of the PCV bottom status for the first time. The status inside the PCV will continue to be examined based on the collected image and dose data.



Capturing the location of fuel debris inside the reactor by measurement using muons

Period	Evaluation results
Feb - May 2015	Confirmed that there was no large fuel in the reactor core.

<Glossarv:

- (*1) TIP (Traversing In-core Probe)
- (*2) Penetration: Through-hole of the PCV
- (*3) S/C (Suppression Chamber): Suppression pool, used as the water source for the emergent core cooling system.
- (*4) SFP (Spent Fuel Pool):
- (*5) RPV (Reactor Pressure Vessel)
- (*6) PCV (Primary Containment Vessel)

March 25, 2021

Secretariat of the Team for Countermeasures for Decommissioning and Contaminated Water Treatment

Immediate target

Identify the plant status and commence R&D and decontamination toward fuel debris retrieval

Installation of an RPV thermometer and permanent PCV supervisory instrumentation


- (1) Replacement of the RPV thermometer
- As the thermometer installed at the Unit 2 RPV bottom after the earthquake had broken in February 2014, it was excluded from the monitoring thermometers.
- In April 2014, removal of the broken thermometer failed and was suspended. Rust-stripping chemicals were injected and the broken thermometer was removed in January 2015. A new thermometer was reinstalled in March. The thermometer has been used as a part of permanent supervisory instrumentation since April.
- (2) Reinstallation of the PCV thermometer and water-level gauge
- Some of the permanent supervisory instrumentation for PCV could not be installed in the planned locations due to interference with existing grating (August 2013). The instrumentation was removed in May 2014 and new instruments were reinstalled in June 2014. The trend of added instrumentation will be monitored for approx. one month to evaluate its validity.
- The measurement during the installation confirmed that the water level inside the PCV was approx. 300mm from the bottom.

Unit 2 Air dose rate inside the Reactor Building: Max. 4.400mSv/h (1F southeast area. upper penetration(1) surface) (measured on November 16, 2011) Reactor Building Front chamber Nitrogen injection flow rate into the RPV(*3): 13.84Nm3/h SFP(*2) temperature: 22.2°C 615 Temperature inside the PCV: approx. 20°C Reactor feed water system: 1.4m3/h Core spray system: 1.4m3/h Temperature of the RPV PCV hydrogen concentration System A: 0.06 vol% bottom: approx. 20°C System B: 0.05 vol% Nitrogen injection flow rate into the PCV(*4): -Nm3/h Water level of the torus chamber: approx TP1.834 (measured on June 6, 2012) Air dose rate inside the PCV: Air dose rate inside the torus chamber: Max. approx. 70Gy/h 30-118mSv/h(measured on April 18, 2012) 6-134mSv/h(measured on April 11, 2013) Temperature inside the PCV: Water level at the triangular corner: TP1.614-1.754 approx. -°C (measured on June 28, 2012) as of 23:00, March 23, 2021) Temperature at the triangular corner: 30.2-32.1°C (measured on June 28, 2012) Water level inside the PCV: Water level of the Turbine Building: -PCV bottom + approx. 300mm (Removal of stagnant water was completed in December 2020) * Indices related to plant are values as of 11:00, March 24, 2021

	1st (Jan 2012)	- Acquiring images - Measuring air temperature			
	2nd (Mar 2012) - Confirming water surface - Measuring water temperature - Measuring				
	3rd (Feb 2013 – Jun 2014)	- Acquiring images - Sampling stagnant water - Measuring water level - Installing permanent monitoring instrumentation			
Investigations inside PCV	4th (Jan – Feb 2017)	- Acquiring images - Measuring dose rate - Measuring air temperature			
	5th (Jan 2018)	- Acquiring images - Measuring dose rate - Measuring air temperature			
	6th (Feb 2019)	- Acquiring images - Measuring dose rate - Measuring air temperature - Grasping characteristics of a portion of deposit			
Leakage points from PCV	- No leakage from torus char	nber rooftop - No leakage from all inside/outside surfaces of S/C			

Investigative results on torus chamber walls

- July 2014, the torus chamber walls were investigated (on the north the east-side walls) using equipment specially developed for that purpose (a swimming robot and a floor traveling robot).
- At the east-side wall pipe penetrations (five points), "the status" and "existence of flow" were checked.
- A demonstration using the above two types of underwater wall investigative equipment showed how the equipment could check the status of penetration.
- · Regarding Penetrations [1]-[5], the results of checking the sprayed tracer (*5) by camera showed no flow around the penetrations. (investigation by the swimming robot)
- Regarding Penetration 3, a sonar check showed no flow around the penetrations. (investigation by the floor traveling robot) Floor traveling robot






Image of the torus chamber east-side cross-sectional investigation

Status of investigation inside the PCV


Prior to fuel debris retrieval, an investigation inside the PCV will be conducted to inspect the status there including the location of fuel debris. [Investigative outline]

- Investigative devices such as a robot will be injected from Unit 2 X-6 penetration⁽¹⁾ and access the inside of the pedestal using the CRD rail. [Progress status]
- On January 26 and 30, 2017, a camera was inserted from the PCV penetration to inspect the status of the CRD replacement rail on which the robot will travel. On February 9, deposit on the access route of the self-propelled investigative device was removed and on February 16, the inside of the PCV was investigated using the device.

 The results of this series of investigations confirmed fallen and deformed gratings and a quantity of deposit inside the pedestal.
- On January 19, 2018, the status below the platform inside the pedestal was investigated using an investigative device with a hanging
 mechanism. From the analytical results of images obtained in the investigation, deposits probably including fuel debris were found at the bottom of the pedestal. In addition, multiple parts higher than the surrounding deposits were also detected. We presumed that there were multiple routes of fuel debris falling. Obtained data were processed in panoramic image visualization to acquire clearer
- · On February 13, 2019, an investigation touching the deposits at the bottom of the pedestal and on the platform was conducted and confirmed that the pebble-shaped deposits, etc. could be moved and that hard rock-like deposits that could not be gripped may exist.
- In addition, images, etc. would help determine the contour and size of the deposits could be collected by moving the investigative unit closer to the deposits than the previous investigation.
- On October 28, 2020, as a preparatory stage of the PCV internal investigation and the trial retrieval, a contact investigation into deposits inside the penetration (X-6 penetration) was conducted. In this investigation, a guide pipe incorporating an investigative unit inserted into the penetration. By the contact, it was confirmed that deposits inside the penetration did not deformed and unstuck.
- On October 30, 2020, a 3D scan investigation was conducted, measuring deposits by the 3D scan sensor mounted on the top of the

Information obtained in the investigation will be utilized in the mockup test of the equipment to remove deposits inside the X-6 penetration.







<Work in front of the penetration>

Capturing the location of fuel debris inside the reactor by measurement using muons

Period	Evaluation results
Mar – Jul 2016	Confirmed the existence of high-density materials, which was considered as fuel debris, at the bottom of RPV, and in the lower part and the outer periphery of the reactor core. It was assumed that a large part of fuel debris existed at the bottom of RPV.

(*2) SFP (Spent Fuel Pool) (*3) RPV (Reactor Pressure Vessel) 1) Penetration: Through-hole of the PCV (*4) PCV (Primary Containment Vessel) (*5) Tracer: Material used to trace the fluid flow. Clay particles

Immediate target

inside PCV

Leakage points

from PCV

2nd (Jul 2017)

Identify the plant status and commence R&D and decontamination toward fuel debris retrieval

Secretariat of the Team for Countermeasures for Decommissioning and Contaminated Water Treatment


Water flow was detected from the Main Steam Isolation Valve* room

On January 18, 2014, a flow of water from around the door of the Steam Isolation Valve room in the Reactor Building Unit 3 1st floor northeast area to the nearby floor drain funnel (drain outlet) was detected. As the drain outlet connects with the underground part of the Reactor Building, there is no possibility of outflow from the building.

From April 23, 2014, image data has been acquired by camera and the radiation dose measured via pipes for measurement instrumentation, which connect the air-conditioning room on the Reactor Building 2nd floor with the Main Steam Isolation Valve Room on the 1st floor. On May 15, 2014, water flow from the expansion joint of one Main Steam Line was detected.

This is the first leak from PCV detected in the Unit 3. Based on the images collected in this investigation, the leak volume will be estimated and the need for additional investigations will be examined. The investigative results will also be utilized to examine water stoppage and PCV repair

* Main Steam Isolation Valve: A valve to shut off the steam generated from the Reactor in an emergency

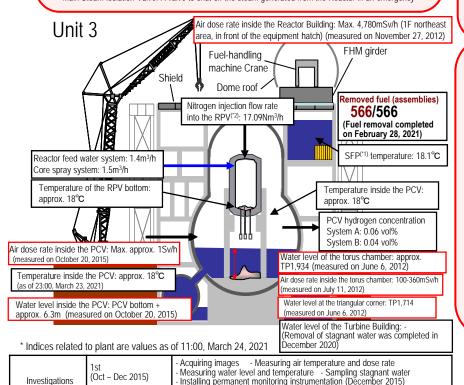

Acquiring images

Main steam pipe bellows (identified in May 2014)


Installing permanent monitoring instrumentation (August 2017)

Investigative results into the Unit 3 PCV equipment hatch using a small investigation device

· As part of the investigation into the PCV to facilitate fuel debris retrieval, the status around the Unit 3 PCV equipment hatch was investigated using a small self-traveling investigation device on November 26, 2015.

· Given blots such as rust identified below the water level inside the PCV, there may be a leakage from the seal to the


extent of bleeding. Methods to investigate and repair the parts, including other PCV penetrations with a similar structure, will be considered.



Investigation inside the PCV

Prior to fuel debris retrieval, the inside of the Primary Containment Vessel (PCV) was investigated to identify the status there including the location of the fuel debris.

- The status of X-53 penetration^('4), which may be under the water and which is scheduled for use to investigate the inside of the PCV, was investigated using remote-controlled ultrasonic test equipment. The results showed that the penetration was not under the water (October 22-24, 2014).
- For the purpose of confirming the status inside the PCV, an investigation device was inserted into the PCV from X-53 penetration on October 20 and 22, 2015 to obtain images, data of dose and temperature and sample stagnant water. No damage was identified on the structure and walls inside the PCV and the water level was almost identical with the estimated value. In addition, the dose inside the PCV was confirmed to be lower than in other Units
- . In July 2017, the inside of the PCV was investigated using the underwater ROV (remotely operated underwater vehicle) to inspect the inside of the pedestal.
- Analysis of image data obtained in the investigation identified damage to multiple structures and the supposed core internals. Consideration about fuel removal based on the obtained information will continue.
- Videos obtained in the investigation were reproduced in 3D. Based on the reproduced images, the relative positions of the structures, such as the rotating platform slipping off the rail with a portion buried in deposits, were visually understood



Capturing the location of fuel debris inside the reactor by measurement using muons

Period	Evaluation results
May - Sep 2017	The evaluation confirmed that no large lump existed in the core area where fuel had been placed and that part of the fuel debris potentially existed at the bottom of the RPV.

<Glossarv>

(*1) SFP (Spent Fuel Pool) (*2) RPV (Reactor Pressure Vessel) (*3) PCV (Primary Containment Vessel) (*4) Penetration: Through-hole of the PCV

Immediate target

Low-permeable layer

Lower permeable layer

(5) Land-side impermeable wall

Low-permeable layer

Stably continue reactor cooling and stagnant water treatment, and improve reliability

RO

quipme

(existing)

Sea-side impermeable wall

Storage

tank

Work to improve the reliability of the circulation water injection cooling system and pipes to transfer stagnant water.

- Operation of the reactor water injection system using Unit 3 Condensate Storage Tank (CST) as a water source commenced (from July 5, 2013). Compared to the previous systems the reliability of the reactor water injection system was enhanced, e.g. by increasing the amount of water-source storage and enhancing durability.

 To reduce the risk of contaminated-water leakage, the circulation loop was shortened by installing a reverse osmosis (RO) device in the Unit 4 Turbine Building within the circulation.
- loop, comprising the transfer of contaminated water, water treatment and injection into the reactors. Operation of the installed RO device started from October 7 and 24-hour operation started from October 20. Installation of the new RO device inside the building shortened the circulation loop from approx. 3 to 0.8 km.
- To accelerate efforts to reduce the radiation density in stagnant water inside the buildings, circulating purification of stagnant water inside the buildings stared on the Unit 3 and 4 side on February 22 and on the Unit 1 and 2 side on April 11.

SPT

(B)

- For circulating purification, a new pipe (stagnant water purification line) divided from the water treatment equipment outlet line was installed to transfer water purified at the water treatment equipment to the Unit 1 Reactor Building and the Unit 2-4 Turbine Buildings.

 * The entire length of contaminated water transfer.

 * The entire length of contaminated water transfer.

 The risks of stagnant water inside the buildings will continue to be reduced in addition to reduction of its storage : Existing line : RO line inside : Stagnant water the building purification line RO-treated water Process Main Building / High Temperature Incinerator Condensed water RO Sr reduced water R/B

SARRY/ KURION

removal of Cs and Si

* The entire length of contaminated water transfer pipes is approx. 2.1km, including the transfer line of surplus water to the upper heights (approx.

Progress status of dismantling of flange tanks

To facilitate replacement of flanged tanks, dismantling of flanged tanks started in H1 east/H2 areas in May 2015. Dismantling of all flanged tanks was completed in H1 east area (12 tanks) in October 2015, in H2 area (28 tanks) in March 2016, in H4 area (56 tanks) in May 2017, in H3 B area (31 tanks) in September 2017, in H5 and H5 north areas (31 tanks) in June 2018, in G6 area (38 tanks) in July 2018. H6 and H6 north areas (24 tanks) in September 2018 and G4 south area (17 tanks) in March 2019.





Start of dismantling in H1 east area


After dismantling in H1 east area

Completion of purification of contaminated water (RO concentrated salt water)

Contaminated water (RO concentrated salt water) is being treated using seven types of equipment including the multi-nuclide removal equipment (ALPS). Treatment of the RO concentrated salt water was completed on May 27, 2015, with the exception of the remaining water at the tank bottom. The remaining water will be treated sequentially toward dismantling the tanks.

The strontium reduced water from other facilities than the multi-nuclide removal equipment will be re-purified in the multi-nuclide removal equipment to further reduce risks.

Preventing groundwater from flowing into the Reactor Buildings




·Length: approx. 1.500m

(Mountain side

Freezing plant

Land-side

mpermeable walls



To reduce groundwater flowing into the buildings, pumping-up of groundwater from wells (subdrains) around the buildings started on September 3, 2015. Pumped-up groundwater was purified at dedicated facilities and released after TEPCO and a third-party organization confirmed that its quality met operational targets.

Via a groundwater bypass, reduce the groundwater level around the Building and groundwater inflow into the Building

Measures to pump up groundwater flowing from the mountain side upstream of the Building to reduce the groundwater inflow (groundwater bypass) have been implemented

The pumped up groundwater is temporarily stored in tanks and released after TEPCO and a thirdparty organization have confirmed that its quality meets operational targets.

Through periodical monitoring, pumping of wells and tanks is operated appropriately. At the observation holes installed at a height equivalent to the buildings, the trend showing a decline in groundwater levels is checked.


The analytical results on groundwater inflow into the buildings based on existing data showed a declining trend.

Installing land-side impermeable walls with frozen soil around Units 1-4 to prevent the inflow of groundwater into the building

To prevent the inflow of groundwater into the buildings, installation of impermeable walls on the land side is planned. Freezing started on the sea side and at a part of the mountain side from March 2016 and at 95% of the mountain side from June 2016. Freezing of the remaining unfrozen sections advanced with a phased approach and freezing of all sections started in August 2017.

In March 2018, construction of the land-side impermeable walls was completed, except for a portion of the depth, based on a monitoring result showing that the underground temperature had declined below 0°C in almost all areas, while on the mountain side, the difference between the inside and outside increased to approx. 4-5 m. The 21st Committee on Countermeasures for Contaminated Water Treatment, held on March 7, 2018, evaluated that together with the function of sub-drains, etc., a water-level management system to stably control groundwater and isolate the buildings from it had been established and had allowed a significant reduction in the amount of contaminated water generated. For the unfrozen depth, a supplementary method was implemented and it was

confirmed that temperature of the part declined below 0°C by September 2018. From February 2019, maintenance operation started at all sections.

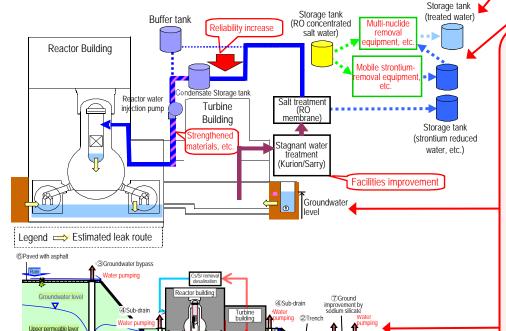

⑤Land-side impermeable wall

Immediate targets

- Reduce the effect of additional release from the entire power station and radiation from radioactive waste (secondary water treatment waste, rubble, etc.) generated after the accident, to limit the effective radiation dose to below 1mSv/year at the site boundaries.
- Prevent contamination expansion in sea, decontamination within the site

Optimization of radioactive protective equipment Based on the progress of measures to reduce environmental dosage on site, the site is categorized into two zones: highly contaminated area around Unit 1-4 buildings, etc. and other areas to optimize protective equipment according to each category aiming at improving safety and productivity by reducing load during work. From March 2016, limited operation started. From March and September 2017, the G Zone was expanded Rzono [Anorak area] %1 Yzono [Coveral area] %2 Gzono [General war area] %3 Line 1 see size Line 3 see size (size 2 Sm above see cvo) (size 2 Sm above see cvo) portal or site firsts for work planning. In addition to the area specified above, when engaging in service contact to regime their barrellar lines with as concentrated with water off in Grane. The area is negropathy dissignated by 7 years in a contact to a part of the service of the common pool building. R zone Y zone G zone (Anorak area) (Coverall area) (General wear) Full-face mask Full-face or half-face masks Or double coveralls



etc.] (excluding site visits), wear a full-face mask.

"2 For works in tank areas containing concentrated salt water or Sr-treated water (excluding works not handling concentrated salt water, etc., pairol, on-site investigation for work planning, and site visits) and own's related to tank transfer lines, wear a full-face mask.

"3 Specified light works (patrol, monitoring, delivery of goods brought from outside, etc.)

MP-3 9th solid waste storage facilities st - 2nd solid waste 3rd – 8th solid waste storage facilities storage facilities Main Anti-Earthquake Building Main gate Rubble storage area Trimmed trees storage area Rubble storage area (planned) Rubble storage area (before operation) Cesium absorption vessel storage area Sludge storage area Sludge storage area (before operation) Concentrated waste liquid storage area
Used protective clothing storage area

Installation of dose-rate monitors

To help workers in the Fukushima Daiichi Nuclear Power Station precisely understand the conditions of their workplaces, a total of 86 dose-rate monitors were installed by January 4, 2016.

These monitors allow workers to confirm real time on-site dose rates at their workplaces.

Workers are also able to check concentrated data through large-scale displays installed in the Main Anti-Earthquake Building and the access control facility.



Installation of Dose-rate monitor

Installation of sea-side impermeable walls

To prevent the outflow of contaminated water into the sea, sea-side impermeable walls have been installed.

Following the completed installation of steel pipe sheet piles on September 22, 2015, connection of these piles was conducted and connection of sea-side impermeable walls was completed on October 26, 2015. Through these works, closure of sea-side impermeable walls was finished and the contaminated water countermeasures have been greatly advanced.



Installation of steel pipe sheet piles for sea-side impermeable wall

Status of the large rest house

A large rest house for workers was established and its operation commenced on May 31, 2015.

Spaces in the large rest house are also installed for office work and collective worker safety checks as well as taking rest.

On March 1, 2016 a convenience store opened in the large rest house. On April 11, operation of the shower room started. Efforts will continue to improve convenience of workers.

