


Progress Status of Transferring the Water Stored in the Underground Reservoirs (As of 4:00 PM on April 12)

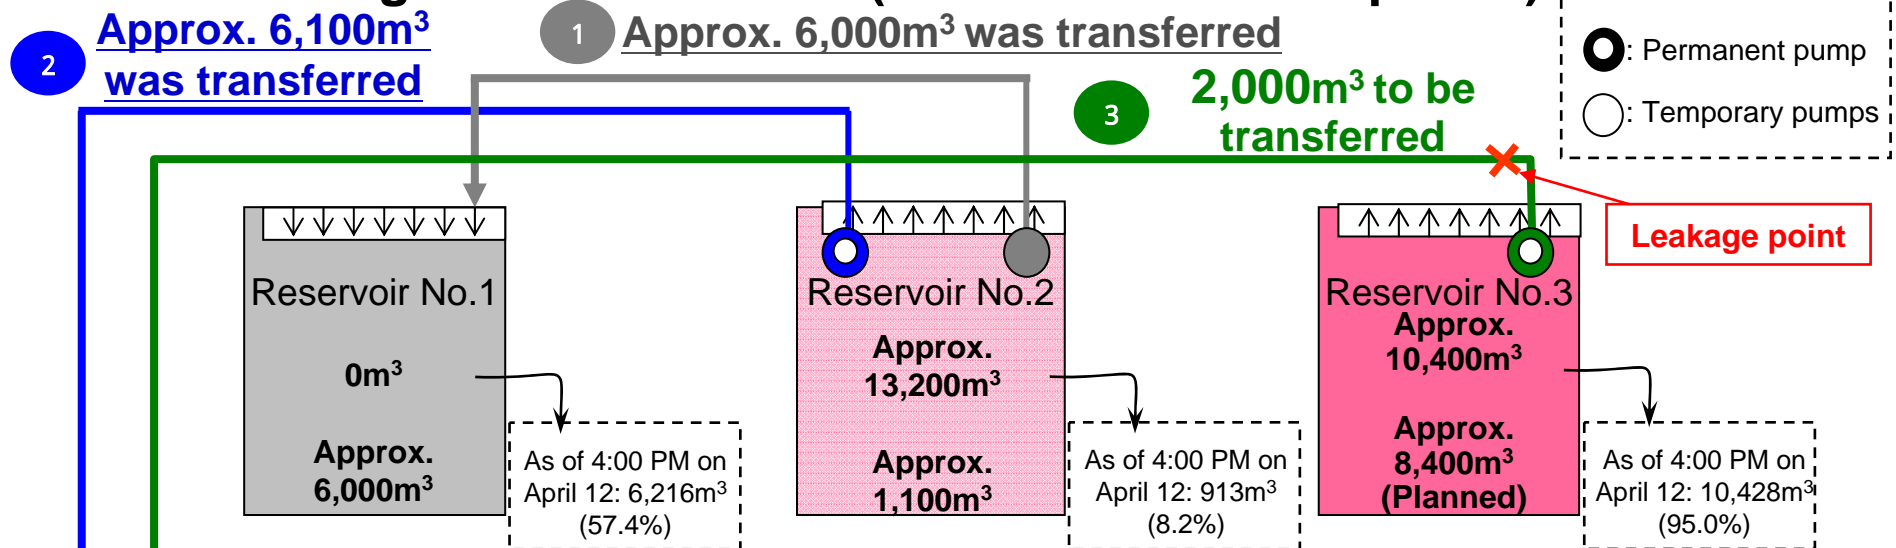

Transfer route	Pump	Progress of transfer	
		Started	Ended
① No.2 No.1	Permanent	4/6 From 5:43	4/6 15:33
	Temporary x 3	4/6 From 9:43	4/6 12:27
	Temporary x 4	4/6 From 12:52 (1) 12:57 (3)	4/8 6:25
	Temporary x 4	4/9 From 10:00	4/9 12:47
② No.2 No.6	Permanent	4/6 From 16:10	4/11 13:06
③ No.3 No.6	Permanent	4/11 From 14:00	4/11 14:03*

* Water transfer from the underground reservoir No.3 to No.6 was suspended due to the water leakage from the pipe.
