
< Reference >
July 17, 2013
Tokyo Electric Power Company

[Progress status of bank protection foundation improvement work between water intakes of Units 1 and 2]

- The foundation improvement was started on July 8, and is currently underway by use of eight foundation improvement machines. (The work starts at 7:00 PM each day and ends at 7:00 AM next day.)
- By the morning of July 17, the work was completed in 38 locations on the sea side line. (The work is planed to cover a total of 231 locations (117 on the sea side line and 114 on the mountain side line))
- We will increase the number of foundation improvement machines to 10 as soon as the additional machines are ready.



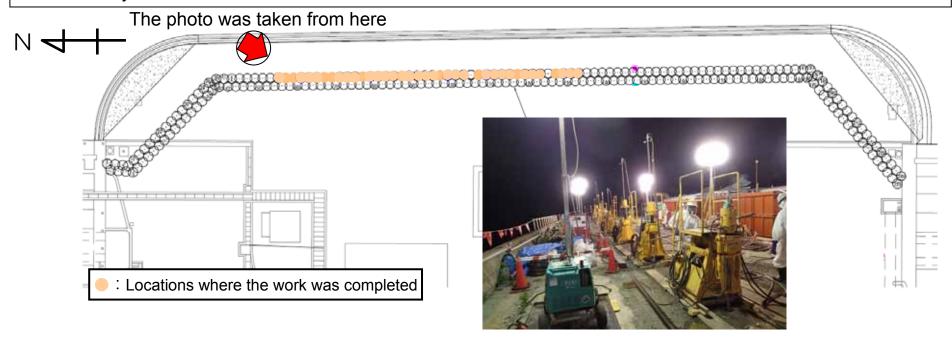

[Conduction of inspections of water intake power cable trenches]

