

Draining Plan between the Water Intake Channel of Unit 1 and Unit 2 at Fukushima Daiichi Nuclear Power Station


<Reference>

August 7, 2013

Tokyo Electric Power Company

[Draining plan between the water intake channel of Unit 1 and 2]

Drilling, gravel filling and pump installation will be performed at the water collecting pit (south) on August 7 and 8. Draining will be performed on August 9. (Transfer to the vertical shaft C is scheduled.)

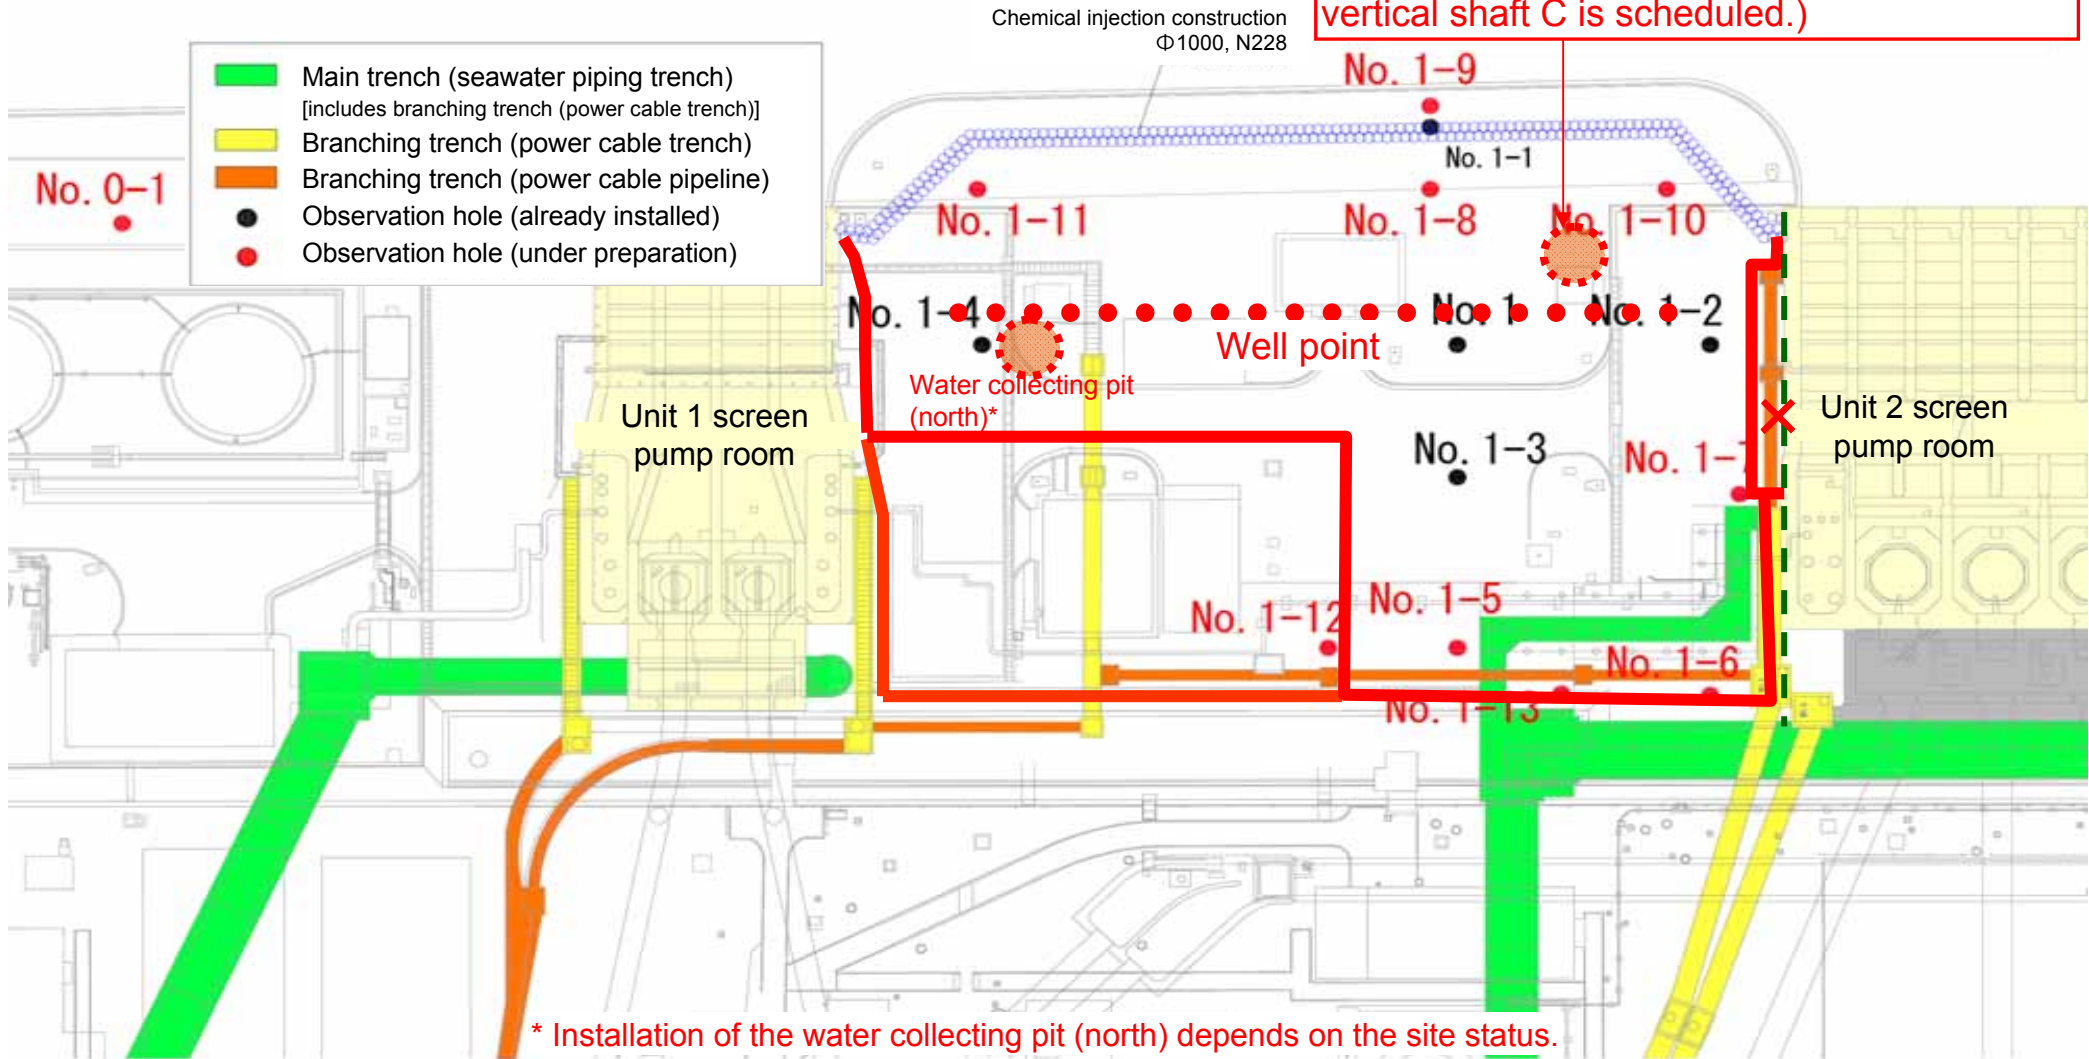

- Construction to install the south side water collecting pit will be started from today (on August 7), and the construction will be continued until August 8.
- Drawing of the groundwater from the water collecting pit will be started from August 9.
- Concurrently, preparation work toward installation of the well point will be started from today (on August 7).

[Reference] Schematic of the well point

