
Changes in the amount of water transferred from groundwater drains to reactor and turbine buildings and in the amount of groundwater and rainwater flowing into the buildings

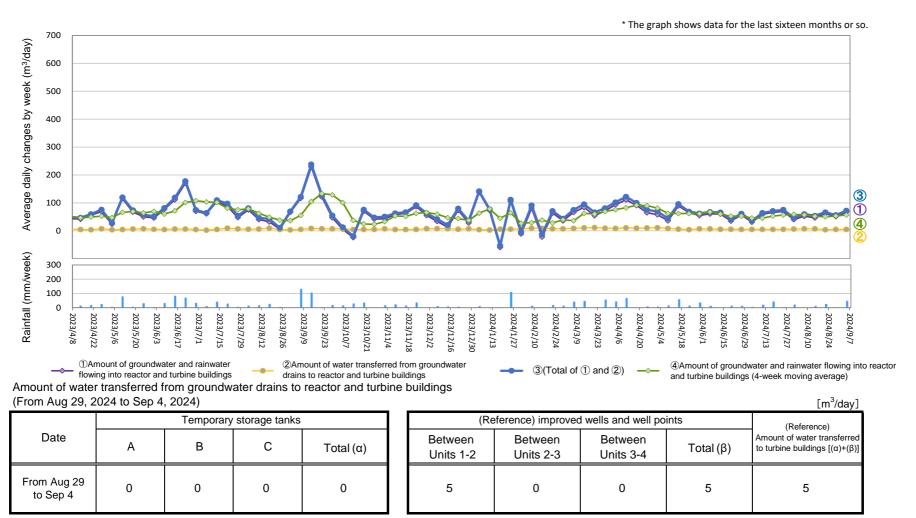

①Amount of groundwater and rainwater flowing into reactor and turbine buildings: 67 m³/day*¹, ②Amount of water transferred from groundwater drains to reactor and turbine buildings: 5 m³/day, ③(Total of ① and ②): 72 m³/day*², Rainfall: 46.5 mm/week

There may be a difference between the sum of the individual data and the total value since the total value is the sum of the data with the first decimal place.

(Reference) (A)Amount of groundwater and rainwater flowing into reactor and turbine buildings (4-week moving average): 57 m³/day^{*3}

^{*} Figures for ①, ③ and ④ have been calculated after elaborating some of cross sectional area of the process main building since April 4, 2024. Nevertheless, figure for ① may be estimated to be a negative value since the calculation still contains uncertainty.

^{*} Values were corrected on September 18, 2024 as follows: *1 from 87 m³/day to 67 m³/day, *2 from 93 m³/day to 72 m³/day, and *3 from 64 m³/day to 57 m³/day.

(Reference) Changes in the amount of water transferred from groundwater drains to reactor and turbine buildings and in the amount of groundwater and rainwater flowing into the buildings from the start of measurement

