Reference

Radioactivity Density of the Seawater in the Port of Fukushima Daiichi NPS < 1/2 >

(Data summarized on March 24)

Place of Sampling	Sh	nallow Draf	t Quay at 1F*		Inside Unit 1-4 Water Intake Canal (North) at 1F		Inside Unit 1-4 Water Intake Canal (North) at 1F (North side of the East Seawall Break)		Seawater Obtained at Unit 1 Screen in 1F		Seawater Obtained at Unit 2 Screen in 1F		② Density Limit Specified by the Reactor Regulation
Time of Sampling	Mar 23, 2014 6:43 AM		N/A		Mar 23, 2014 6:47 AM		Mar 23, 2014 7:13 AM		Mar 23, 2014 6:49 AM		Mar 23, 2014 7:02 AM		(Bq/L) (The density limit in the water outside the
Detected Nuclides (Half-life)	①Density of Sample (Bq/L)	Scaling Factor (①/②)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (①/②)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	surrounding monitored areas is provided in section 6 of Appendix 2.)
I-131 (Approx. 8 days)	ND	-	-	-	ND	-	ND	-	ND	-	ND	-	40
Cs-134 (Approx. 2 years)	ND	-	-	-	14	0.23	8.8	0.15	9.5	0.16	17	0.28	60
Cs-137 (Approx. 30 years)	ND	-	-	-	41	0.46	19	0.21	36	0.40	32	0.36	90

^{*} The density specified by the Reactor Regulation is converted from Bq/cm3 to Bq/L.

As the detection limit may vary depending on the detectors and sample properties, there are cases where nuclides below the detection limit are detected.

^{*} Data of other nuclides is under evaluation.

^{*} In the case of more than 2 nuclides, the sum of scaling factors to density limits is compared to 1.

^{* &}quot;ND" indicates that the measurement result is below the detection limit.

I-131: Approx. 3Bq/L, Cs-134: Approx.2Bq/L, Cs-137: Approx.2Bq/L

^{*} The sampling will be performed after opening and closing of the silt fence.

Reference

Radioactivity Density of the Seawater in the Port of Fukushima Daiichi NPS < 2/2 >

(Data summarized on March 24)

Place of Sampling	Seawater Obtained at Unit 3 Screen in 1F		1F Unit 4 Screen (Outside the Silt Fence)		1F Unit 4 Screen (Inside the Silt Fence)		Inside Unit 1-4 Water Intake Canal (South) at 1F		Port Entrance of Fukushima Daiichi NPS*		In Front of Unit 6* Water Intake Canal at 1F		② Density Limit Specified by the Reactor Regulation (Bq/L) (The density limit in the water outside the
Time of Sampling	Mar 23, 2014 7:04 AM		Mar 23, 2014 7:05 AM		Mar 23, 2014 7:06 AM		Mar 23, 2014 7:09 AM		N/A		N/A		
Detected Nuclides (Half-life)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	surrounding monitored
I-131 (Approx. 8 days)	ND	-	ND	-	ND	-	ND	-	-	-	-	-	40
Cs-134 (Approx. 2 years)	14	0.23	13	0.22	6.6	0.11	11	0.18	-	-	-	-	60
Cs-137 (Approx. 30 years)	37	0.41	35	0.39	23	0.26	28	0.31	-	-	-	-	90

^{*} The density specified by the Reactor Regulation is converted from Bq/cm3 to Bq/L.

As the detection limit may vary depending on the detectors and sample properties, there are cases where nuclides below the detection limit are detected.

^{*} Data of other nuclides is under evaluation.


^{*} In the case of more than 2 nuclides, the sum of scaling factors to density limits is compared to 1.

^{* &}quot;ND" indicates that the measurement result is below the detection limit.


I-131: Approx. 3Bq/L

^{*} The sampling will be performed once a week (it will be performed on the day when opening and closing of the silt fence is conducted.).


Radioactivity Density of the Seawater in Front of the Shallow Draft Quay at 1F (Bq/L)

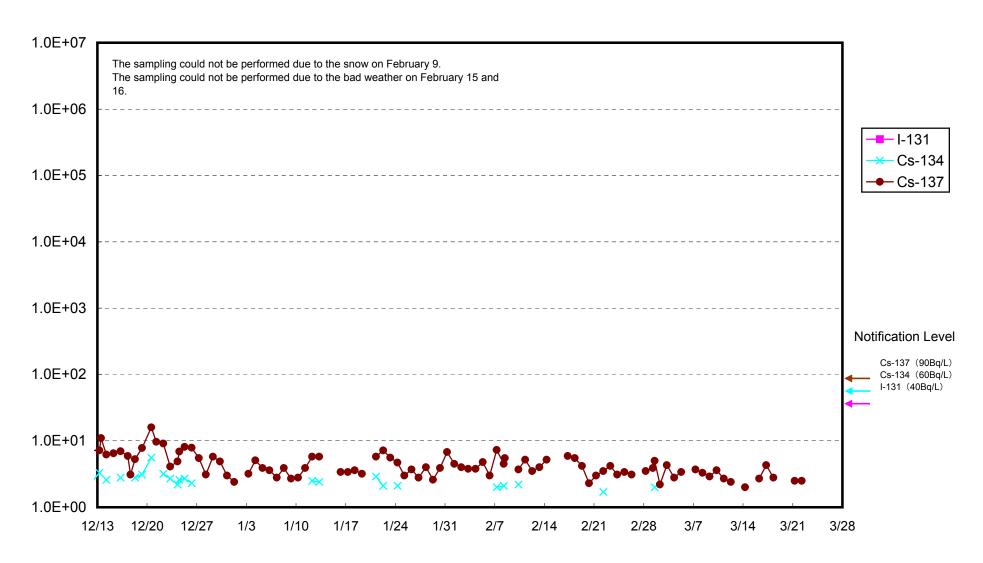


Radioactivity Density of the Seawater at the North of Unit 1-4 Water Intake of Fukushima Daiichi NPS (Bq/L)

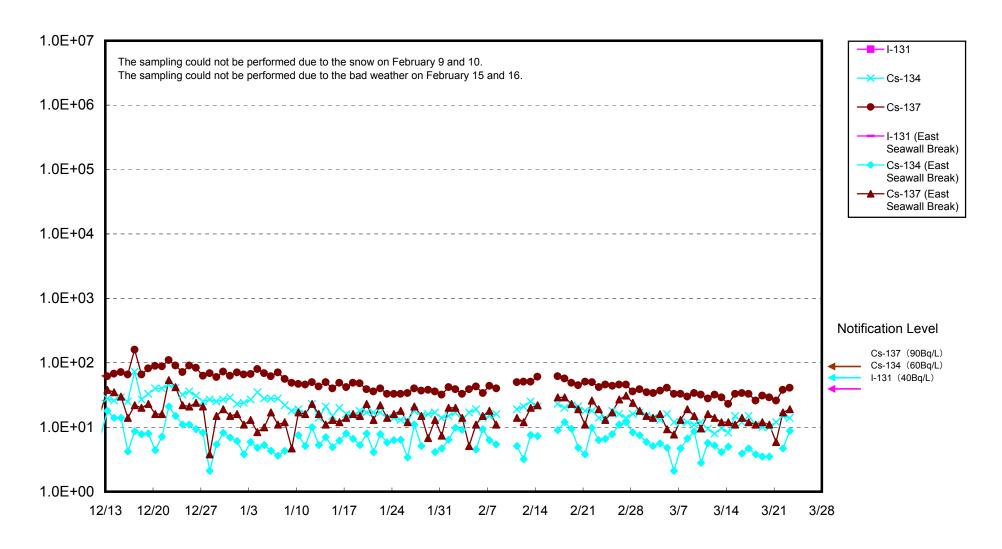


Radioactivity Density of the Seawater Obtained at Unit 1 Screen in Fukushima Daiichi NPS (Bq/L)

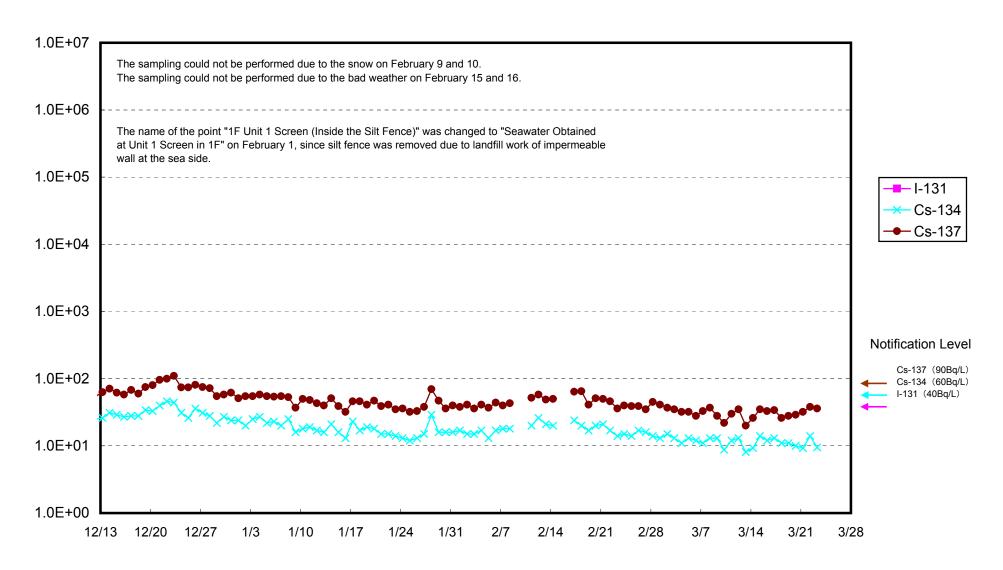


Radioactivity Density of the Seawater Obtained at Unit 2 Screen in Fukushima Daiichi NPS (Bq/L)

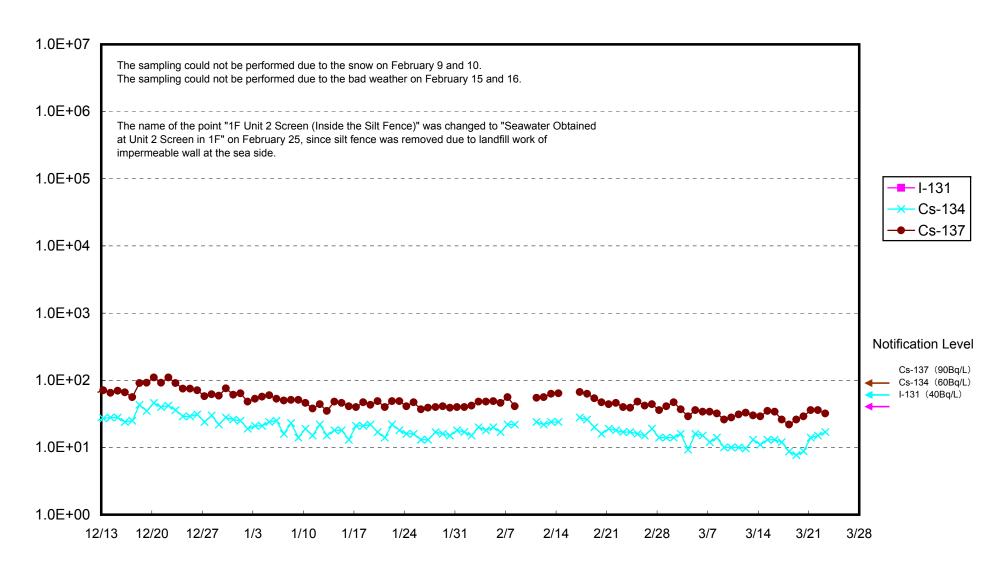


Radioactivity Density of the Seawater Obtained at Unit 3 Screen in Fukushima Daiichi NPS (Bq/L)

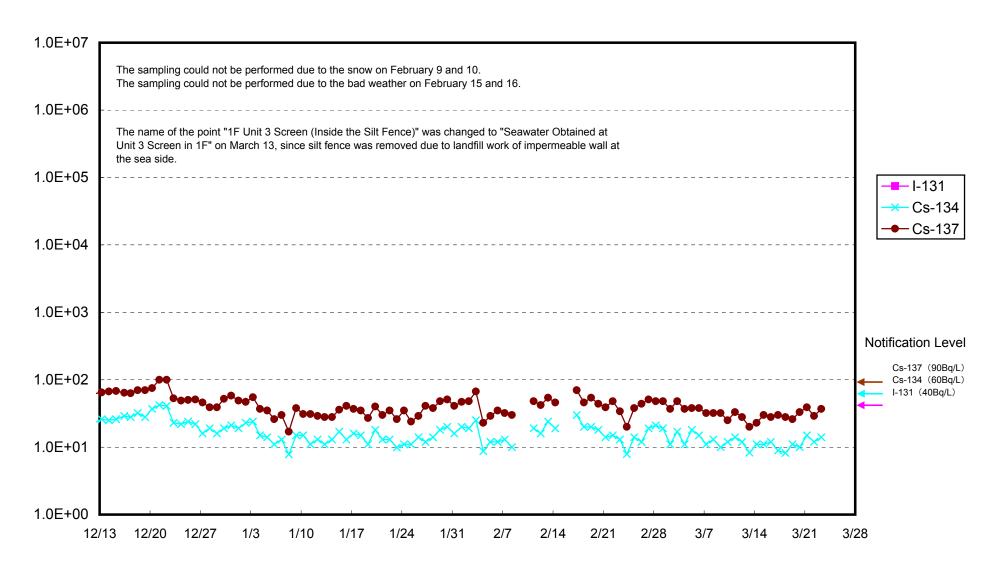

Radioactivity Density of the Seawater at Unit 4 Screen at 1F (Outside the Silt Fence) (Bq/L)

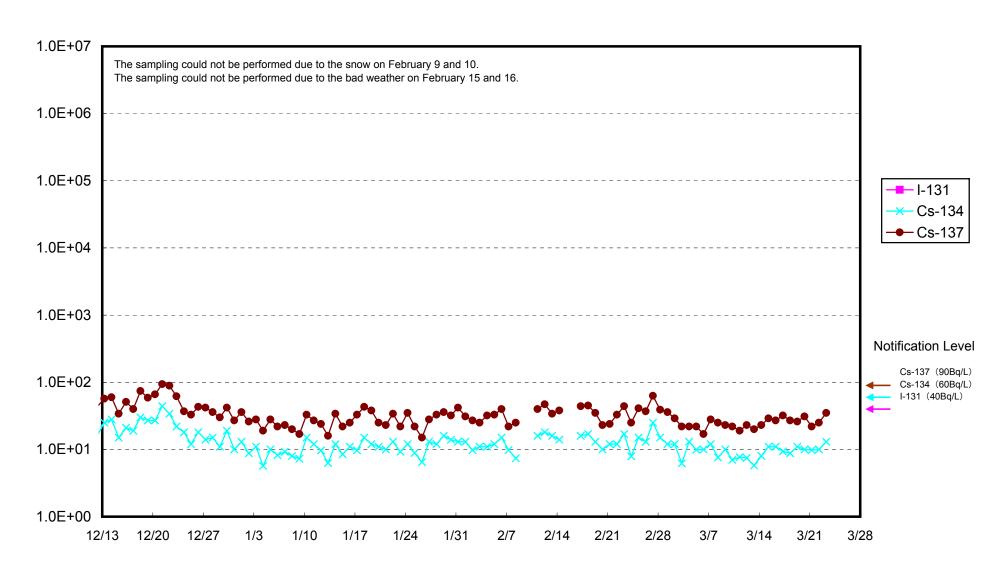

Radioactivity Density of the Seawater at Unit 4 Screen at 1F (Inside the Silt Fence) (Bq/L)

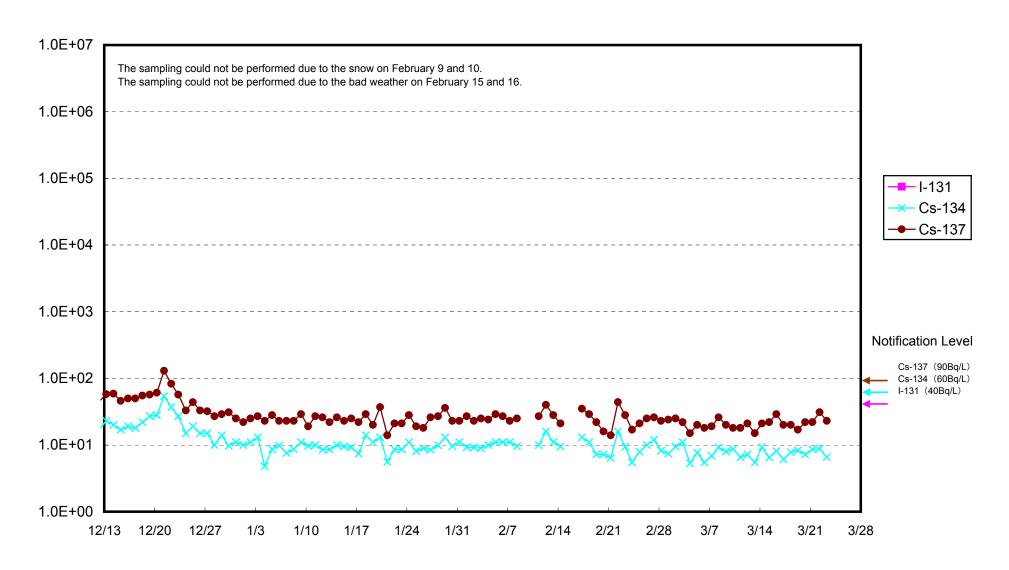

Radioactivity Density of the Seawater at the South of Unit 1-4 Water Intake of Fukushima Daiichi NPS (Bq/L)

