

Result of nuclide analysis of sub drain of Fukushima Daiichi NPS

Reference

(Data summarized on March 20)

Place of Sampling	Fukushima Daiichi NPS 1U sub-drain	Fukushima Daiichi NPS 2U sub-drain	Fukushima Daiichi NPS 3U sub-drain	Fukushima Daiichi NPS 4U sub-drain	Fukushima Daiichi NPS 5U sub-drain	Fukushima Daiichi NPS 6U sub-drain	Fukushima Daiichi NPS Deep well
Time of Sampling	Mar 19, 2012 10:17 am	Mar 19, 2012 10:30 am	Mar 19, 2012 09:55 am	Mar 19, 2012 09:40 am	Mar 19, 2012 09:30 am	Mar 19, 2012 09:25 am	Mar 19, 2012 09:10 am
Detected Nuclides (Half-life)	Density of sample (Bq/cm ³)						
I-131 (about 8 days)	ND	ND	ND	ND	ND	ND	ND
Cs-134 (about 2 years)	6.3E-01	4.2E-01	ND	ND	ND	ND	ND
Cs-137 (about 30 years)	9.9E-01	6.6E-01	ND	ND	ND	ND	ND

* 0.0E-0 means 0.0 x 10-0


* Data of other nuclides are under evaluation.

* "ND" means the sampled data is below measurable limit.


I-131: approx. 2E-2Bq/cm³, Cs-134: approx. 2E-2Bq/cm³, Cs-137: approx. 3E-2Bq/cm³)

Please note that these nuclides are sometimes detected even when they are below the limits, contingent on the detector or samples.


Fukushima Daiichi Nuclear Power Station : Radioactivity Density of Sub-drain at Unit 1 (Bq/cm³)

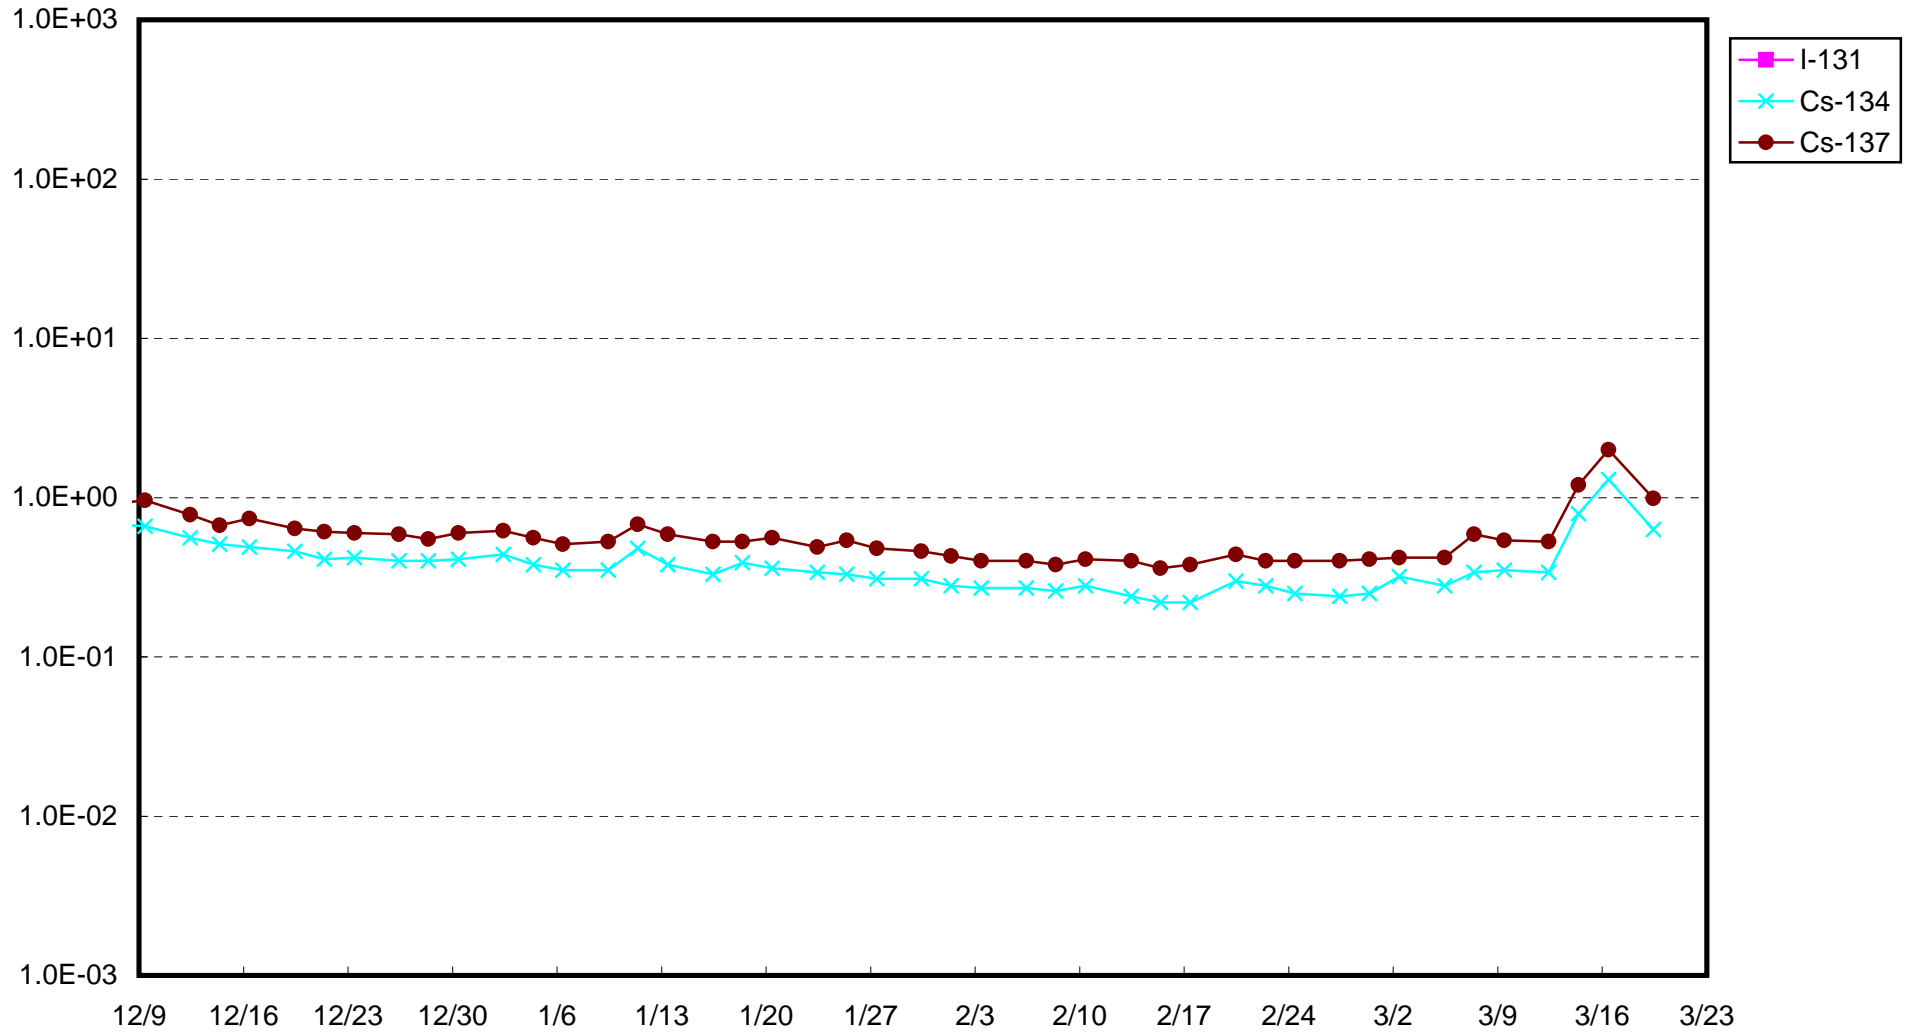


Fukushima Daiichi Nuclear Power Station : Radioactivity Density of Sub-drain at Unit 2 (Bq/cm³)

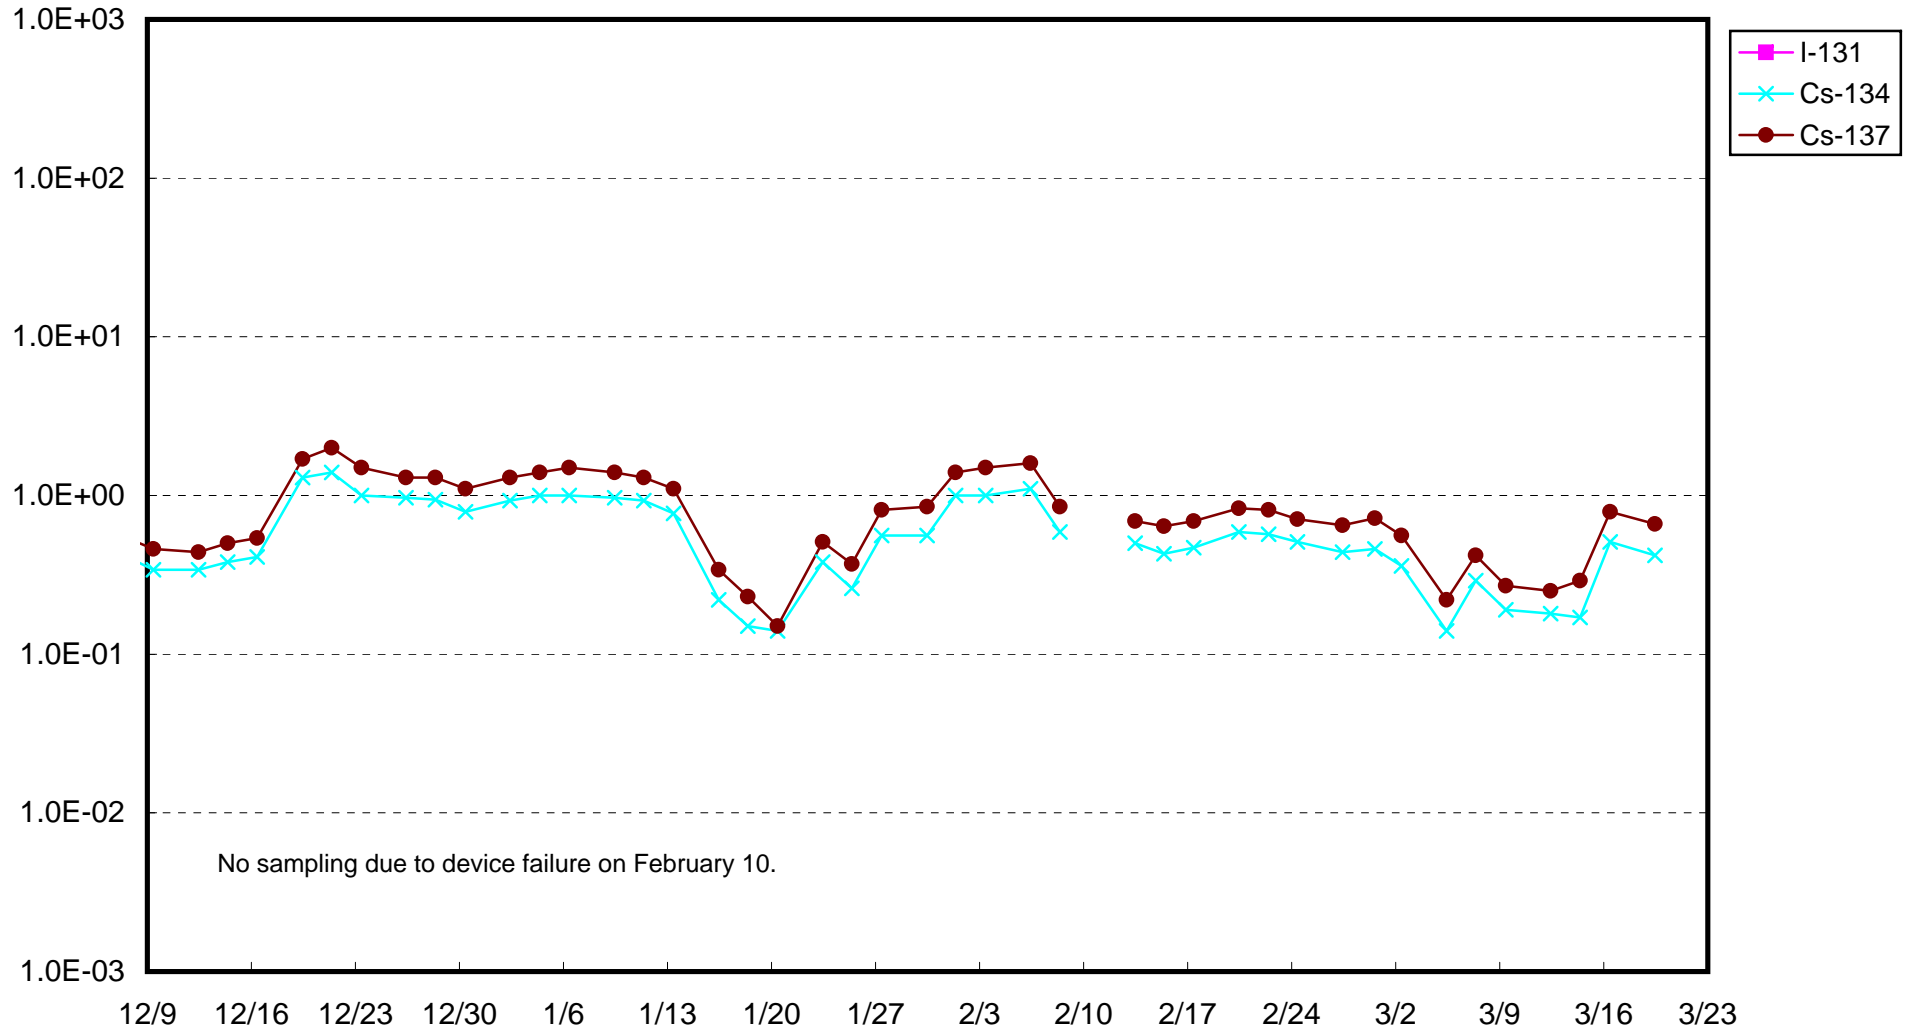


Fukushima Daiichi Nuclear Power Station : Radioactivity Density of Sub-drain at Unit 3 (Bq/cm³)

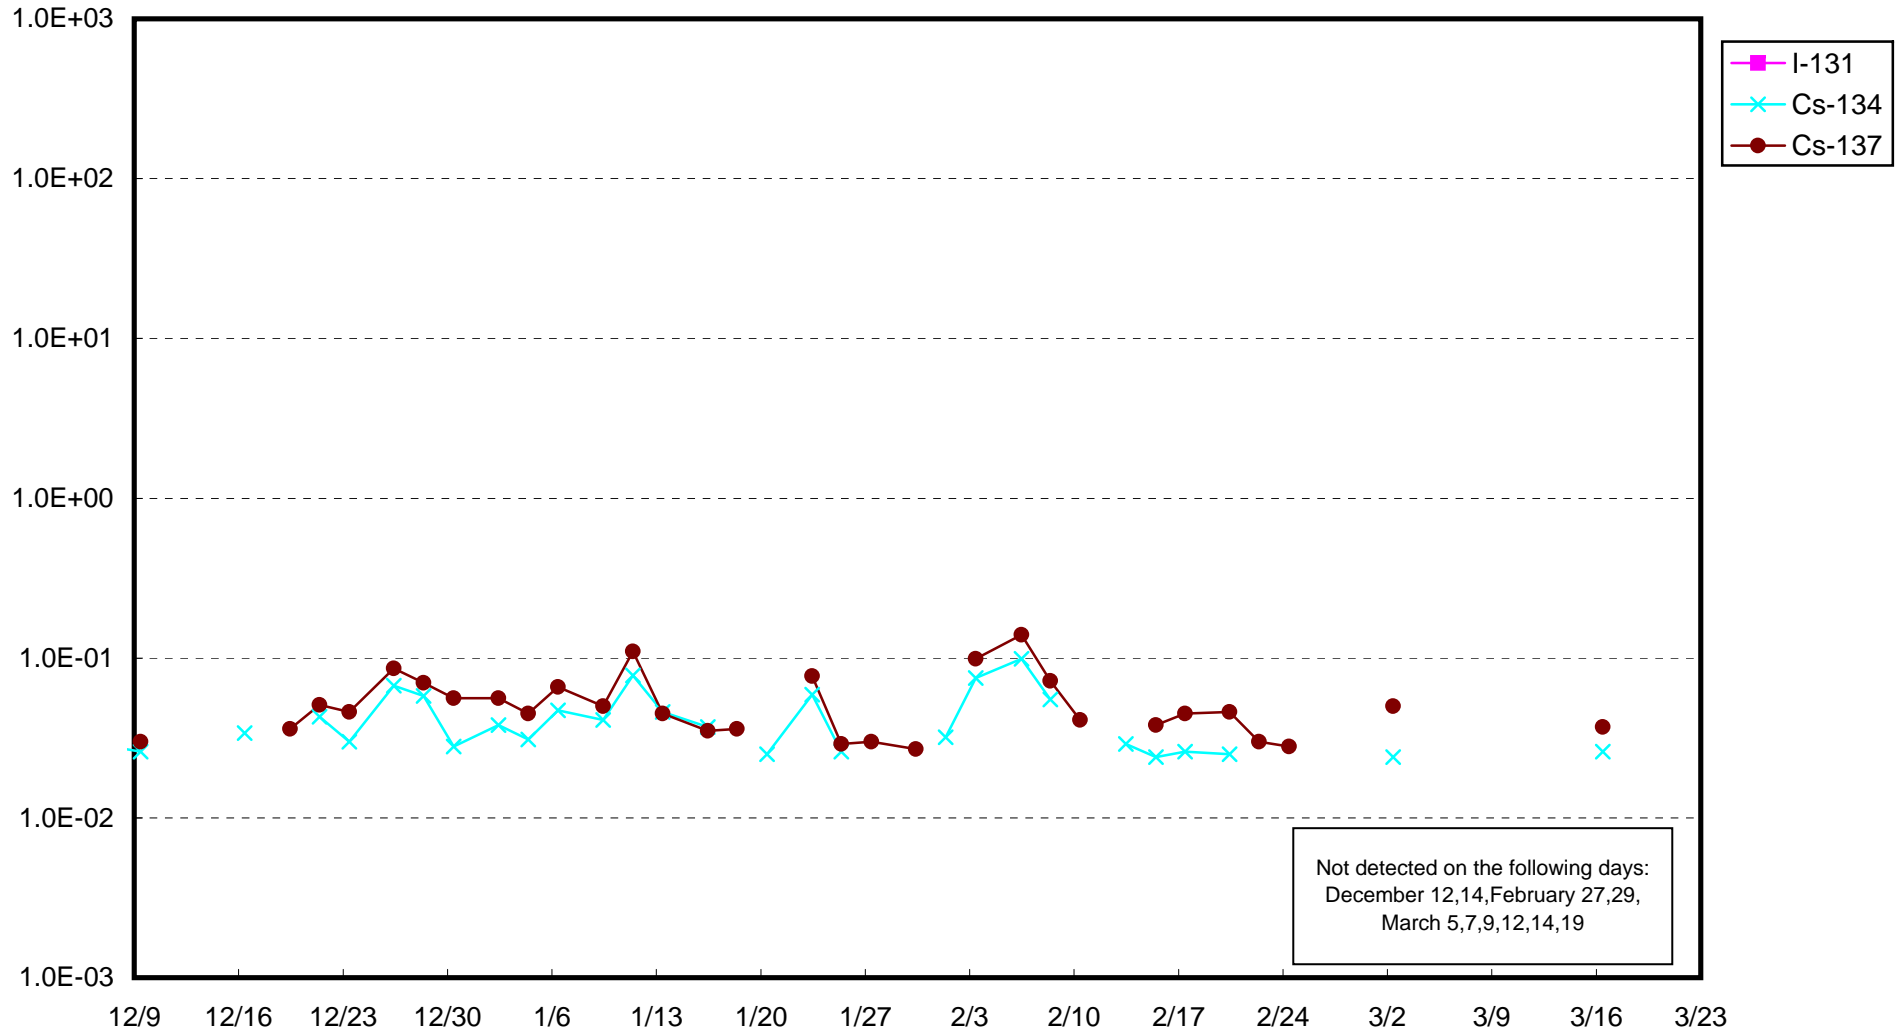


Fukushima Daiichi Nuclear Power Station : Radioactivity Density of Sub-drain at Unit 4 (Bq/cm³)

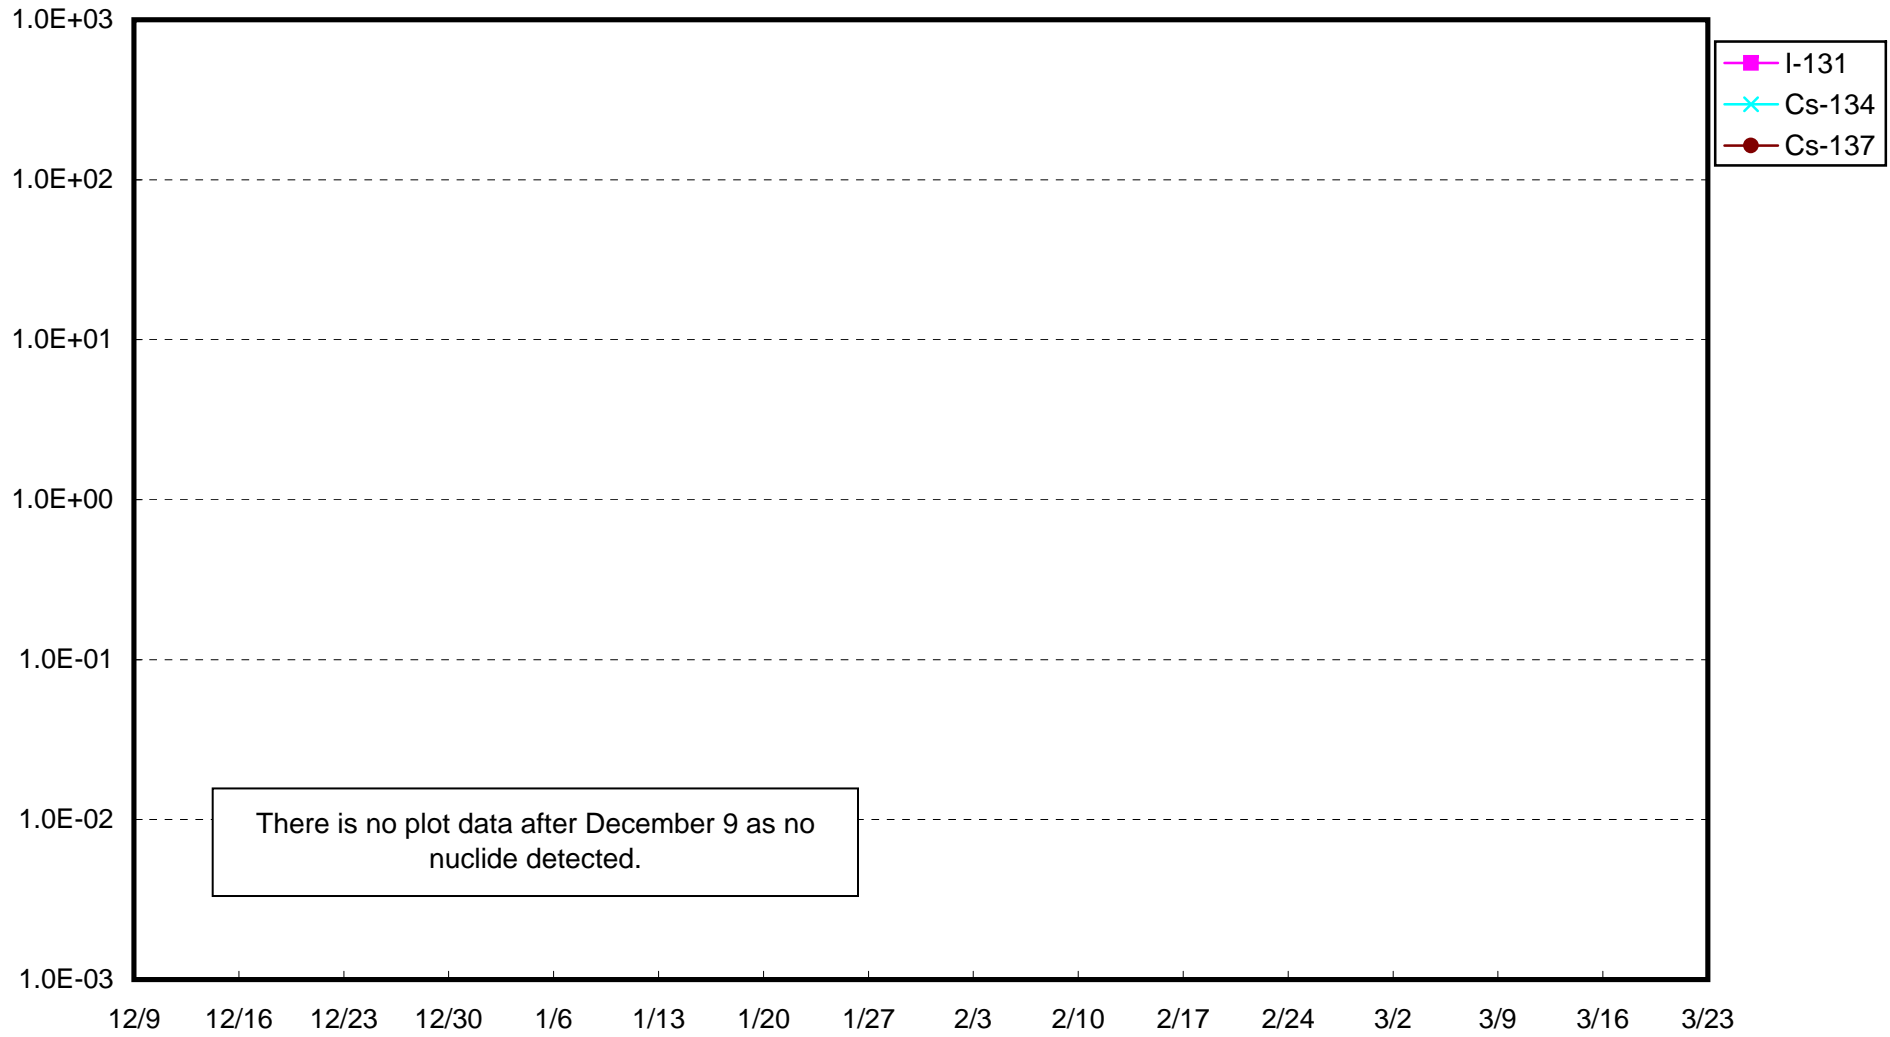

Fukushima Daiichi Nuclear Power Station : Radioactivity Density of Sub-drain at Unit 5 (Bq/cm³)

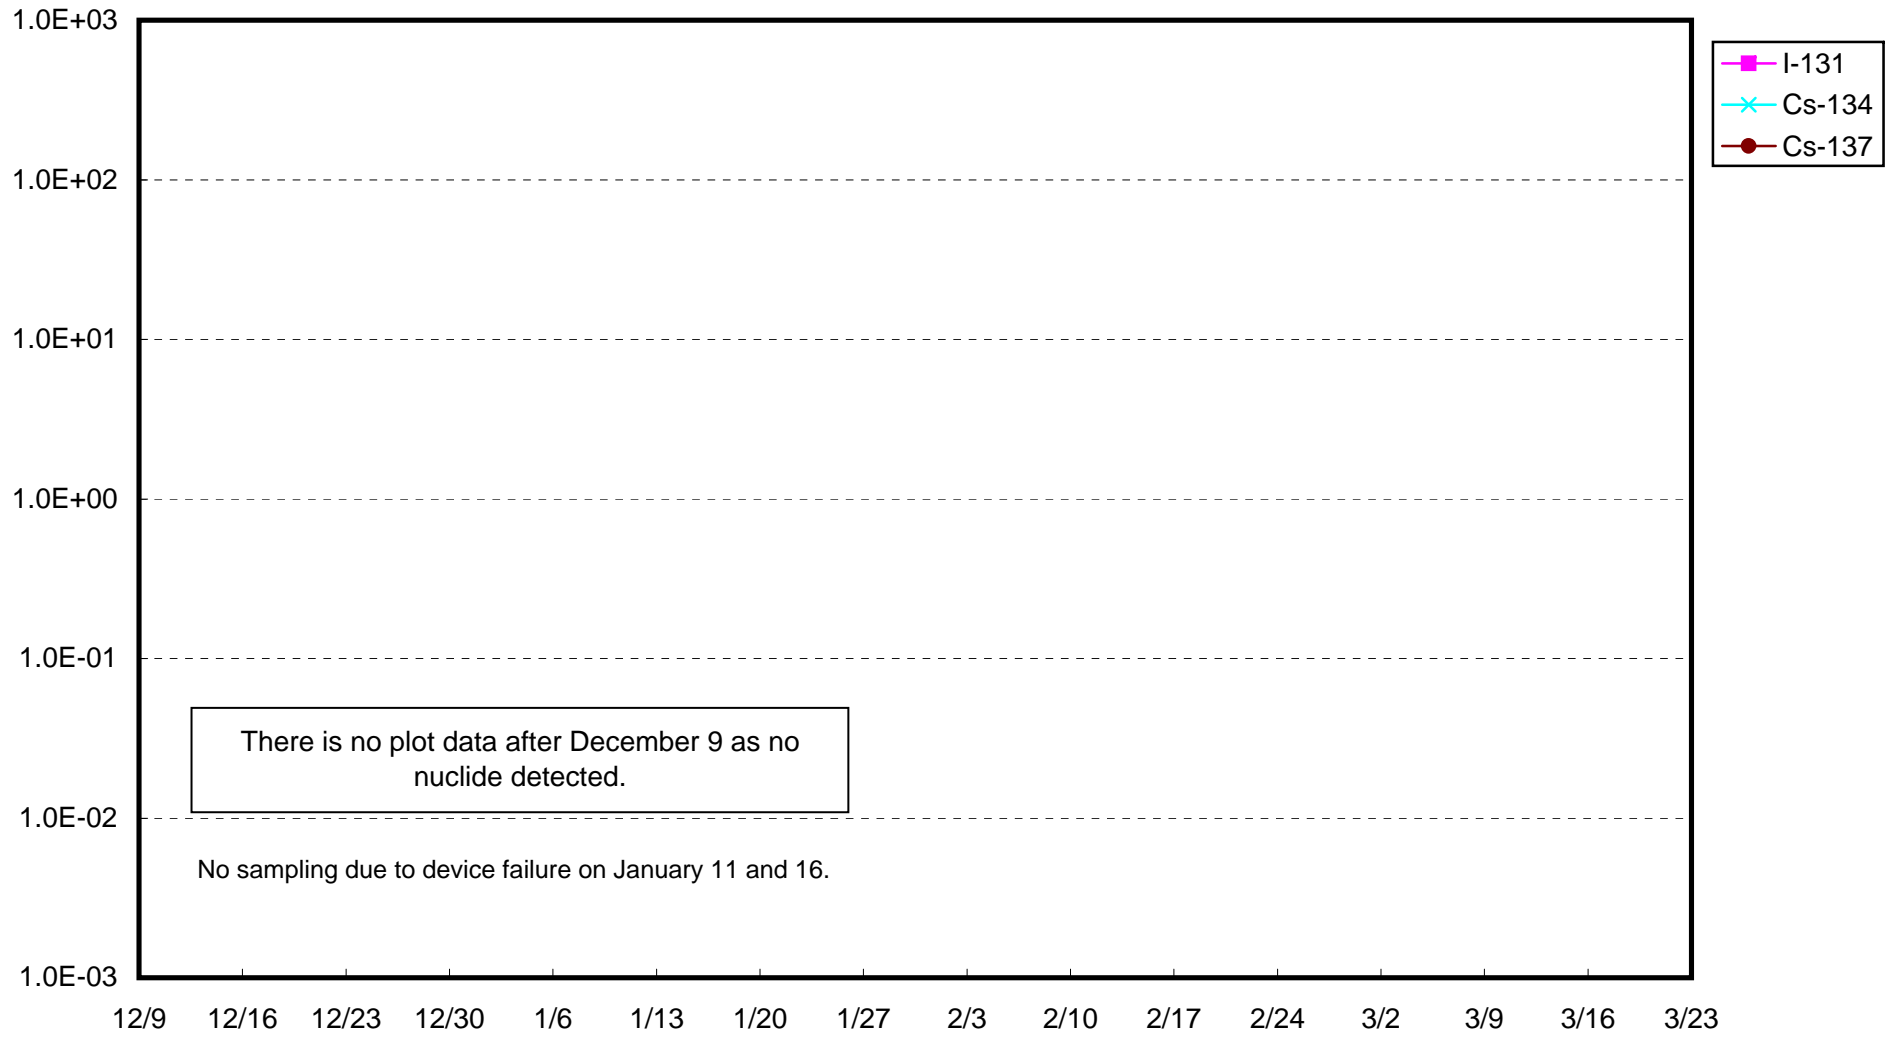

Fukushima Daiichi Nuclear Power Station : Radioactivity Density of Sub-drain at Unit 6 (Bq/cm³)

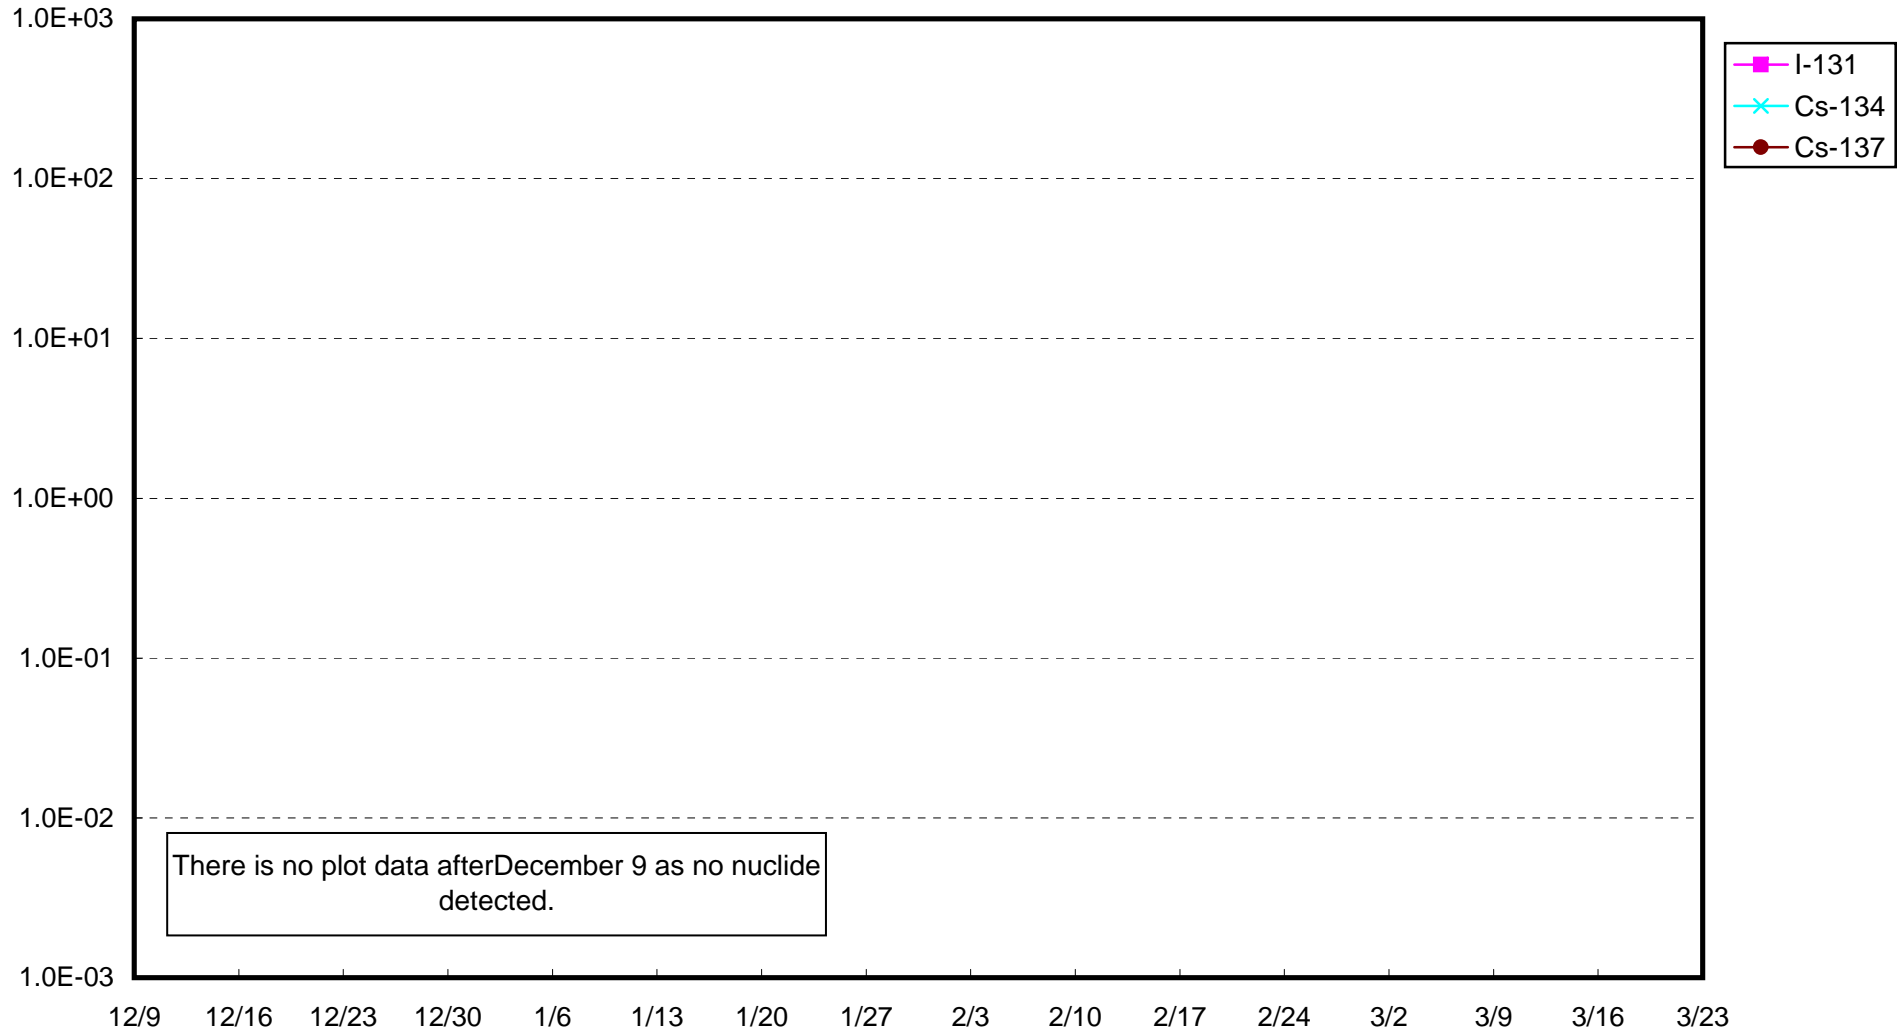

Fukushima Daiichi Nuclear Power Station : Radioactivity Density at the Deep Well at the Site (Bq/cm³)

