


Fukushima Daiichi NPS Survey Map (As of 5:00 PM on June 17, 2013)

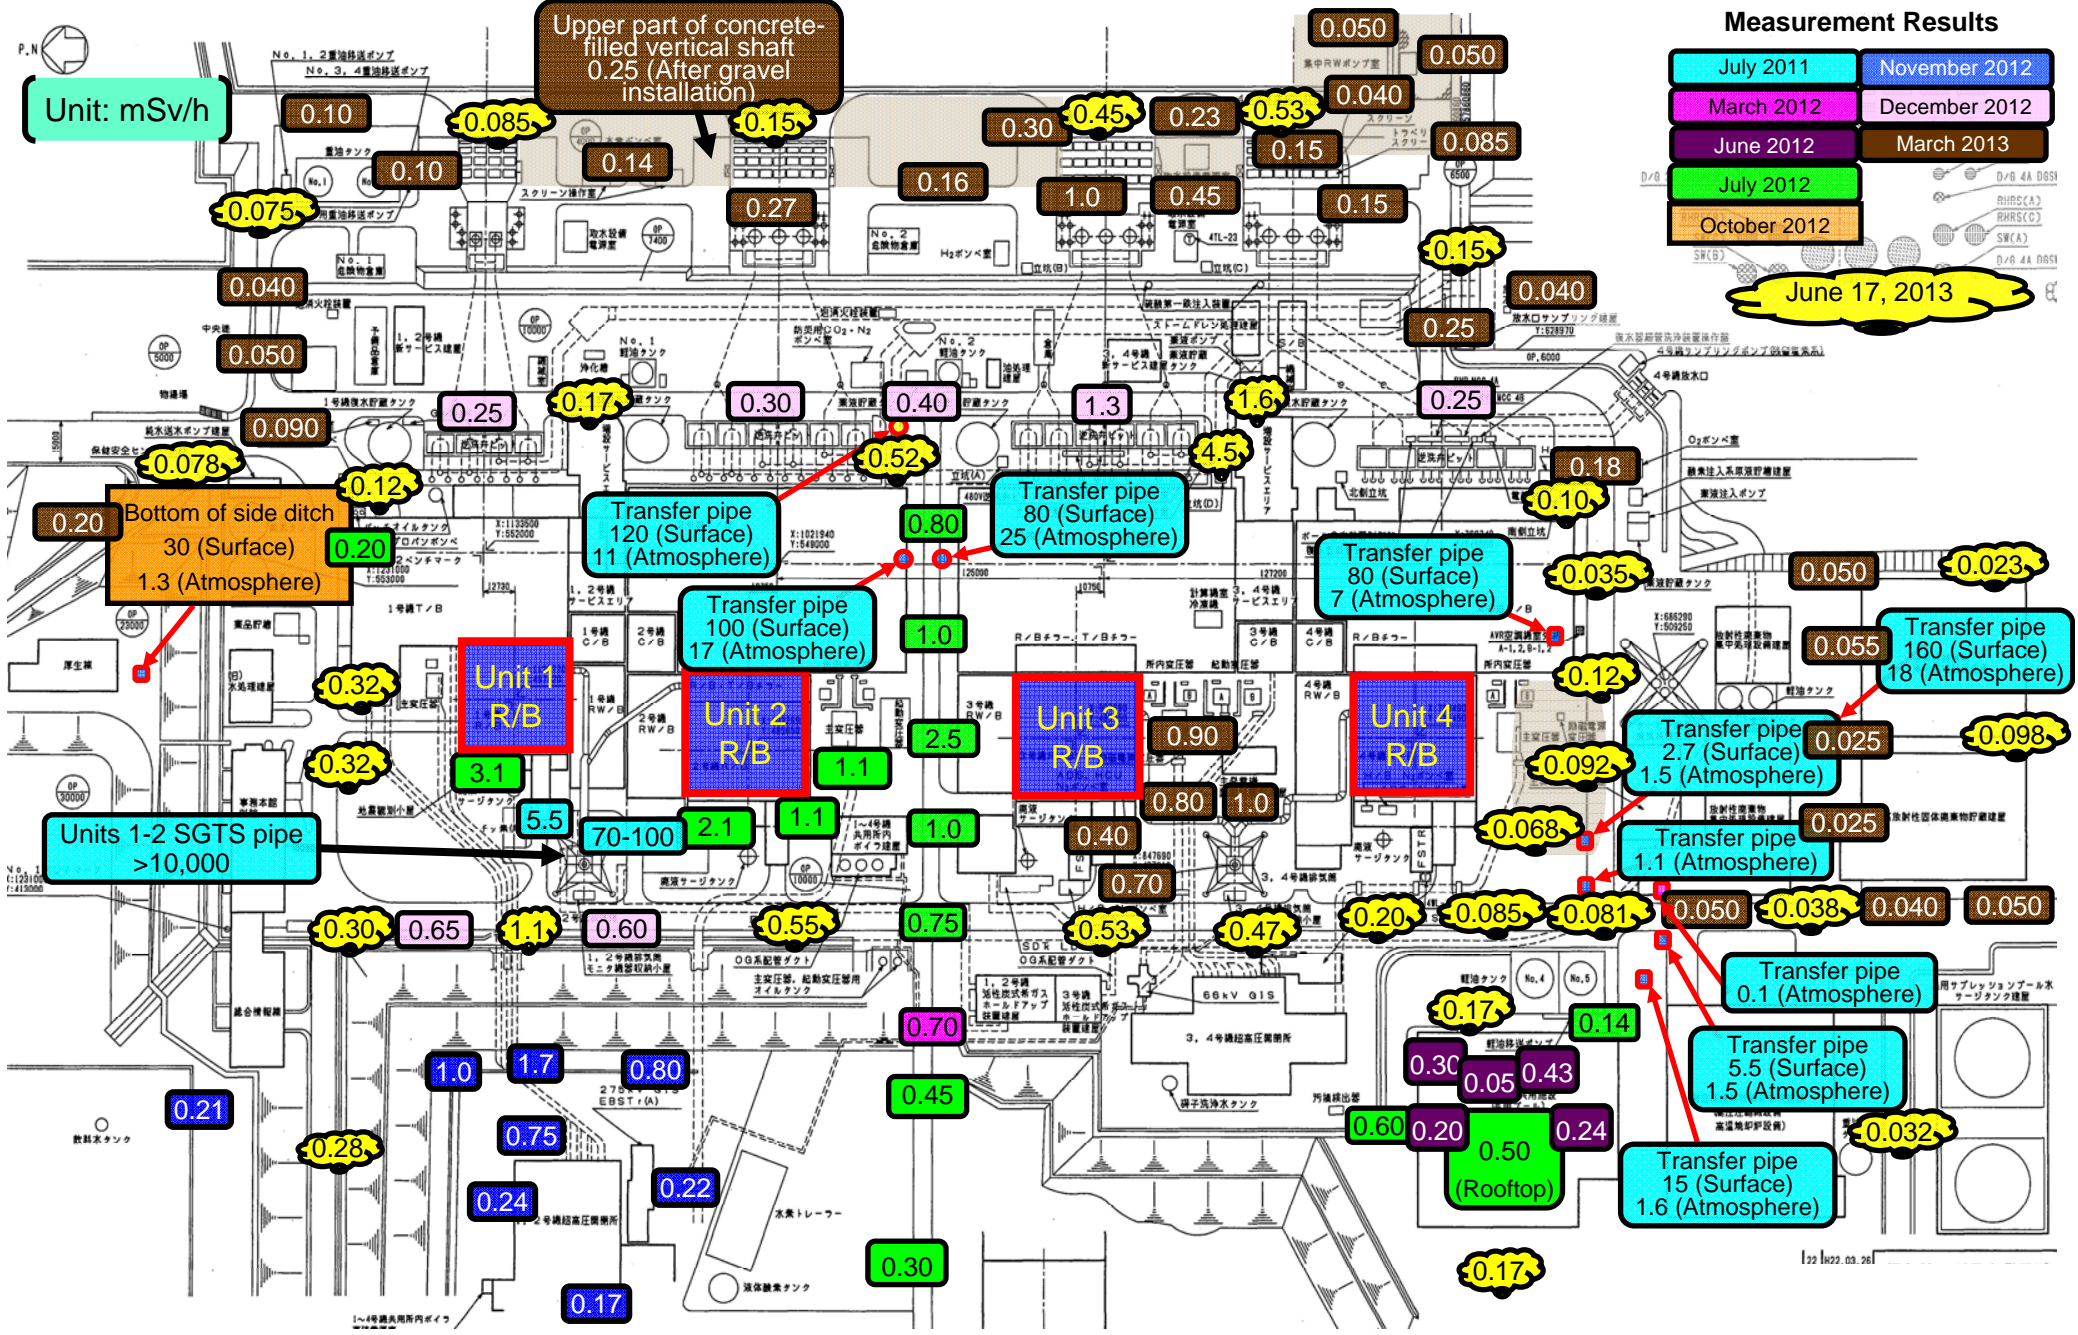

Measurement Results

July 2011	November 2012
March 2012	December 2012
June 2012	March 2013
July 2012	
October 2012	
June 17, 2013	

Unit: mSv/h

Upper part of concrete-filled vertical shaft
0.25 (After gravel installation)

Bottom of side ditch
30 (Surface)
1.3 (Atmosphere)

Transfer pipe
120 (Surface)
11 (Atmosphere)

Transfer pipe
80 (Surface)
25 (Atmosphere)

Transfer pipe
80 (Surface)
7 (Atmosphere)

Transfer pipe
100 (Surface)
17 (Atmosphere)

Transfer pipe
160 (Surface)
18 (Atmosphere)

Unit 1
R/B

Unit 2
R/B

Unit 3
R/B

Unit 4
R/B

Transfer pipe
2.7 (Surface)
1.5 (Atmosphere)

Units 1-2 SGTS pipe
>10,000

Transfer pipe
1.1 (Atmosphere)

Transfer pipe
0.1 (Atmosphere)

Transfer pipe
5.5 (Surface)
1.5 (Atmosphere)

Transfer pipe
15 (Surface)
1.6 (Atmosphere)

0.50
(Rooftop)
