<Reference>
June 28, 2014
Tokyo Electric Power Company

Detailed Analysis Results in the Port of Fukushima Daiichi NPS, around Discharge Channel and Bank Protection (Sampling Locations of Underground Water Obtained at Bank Protection)

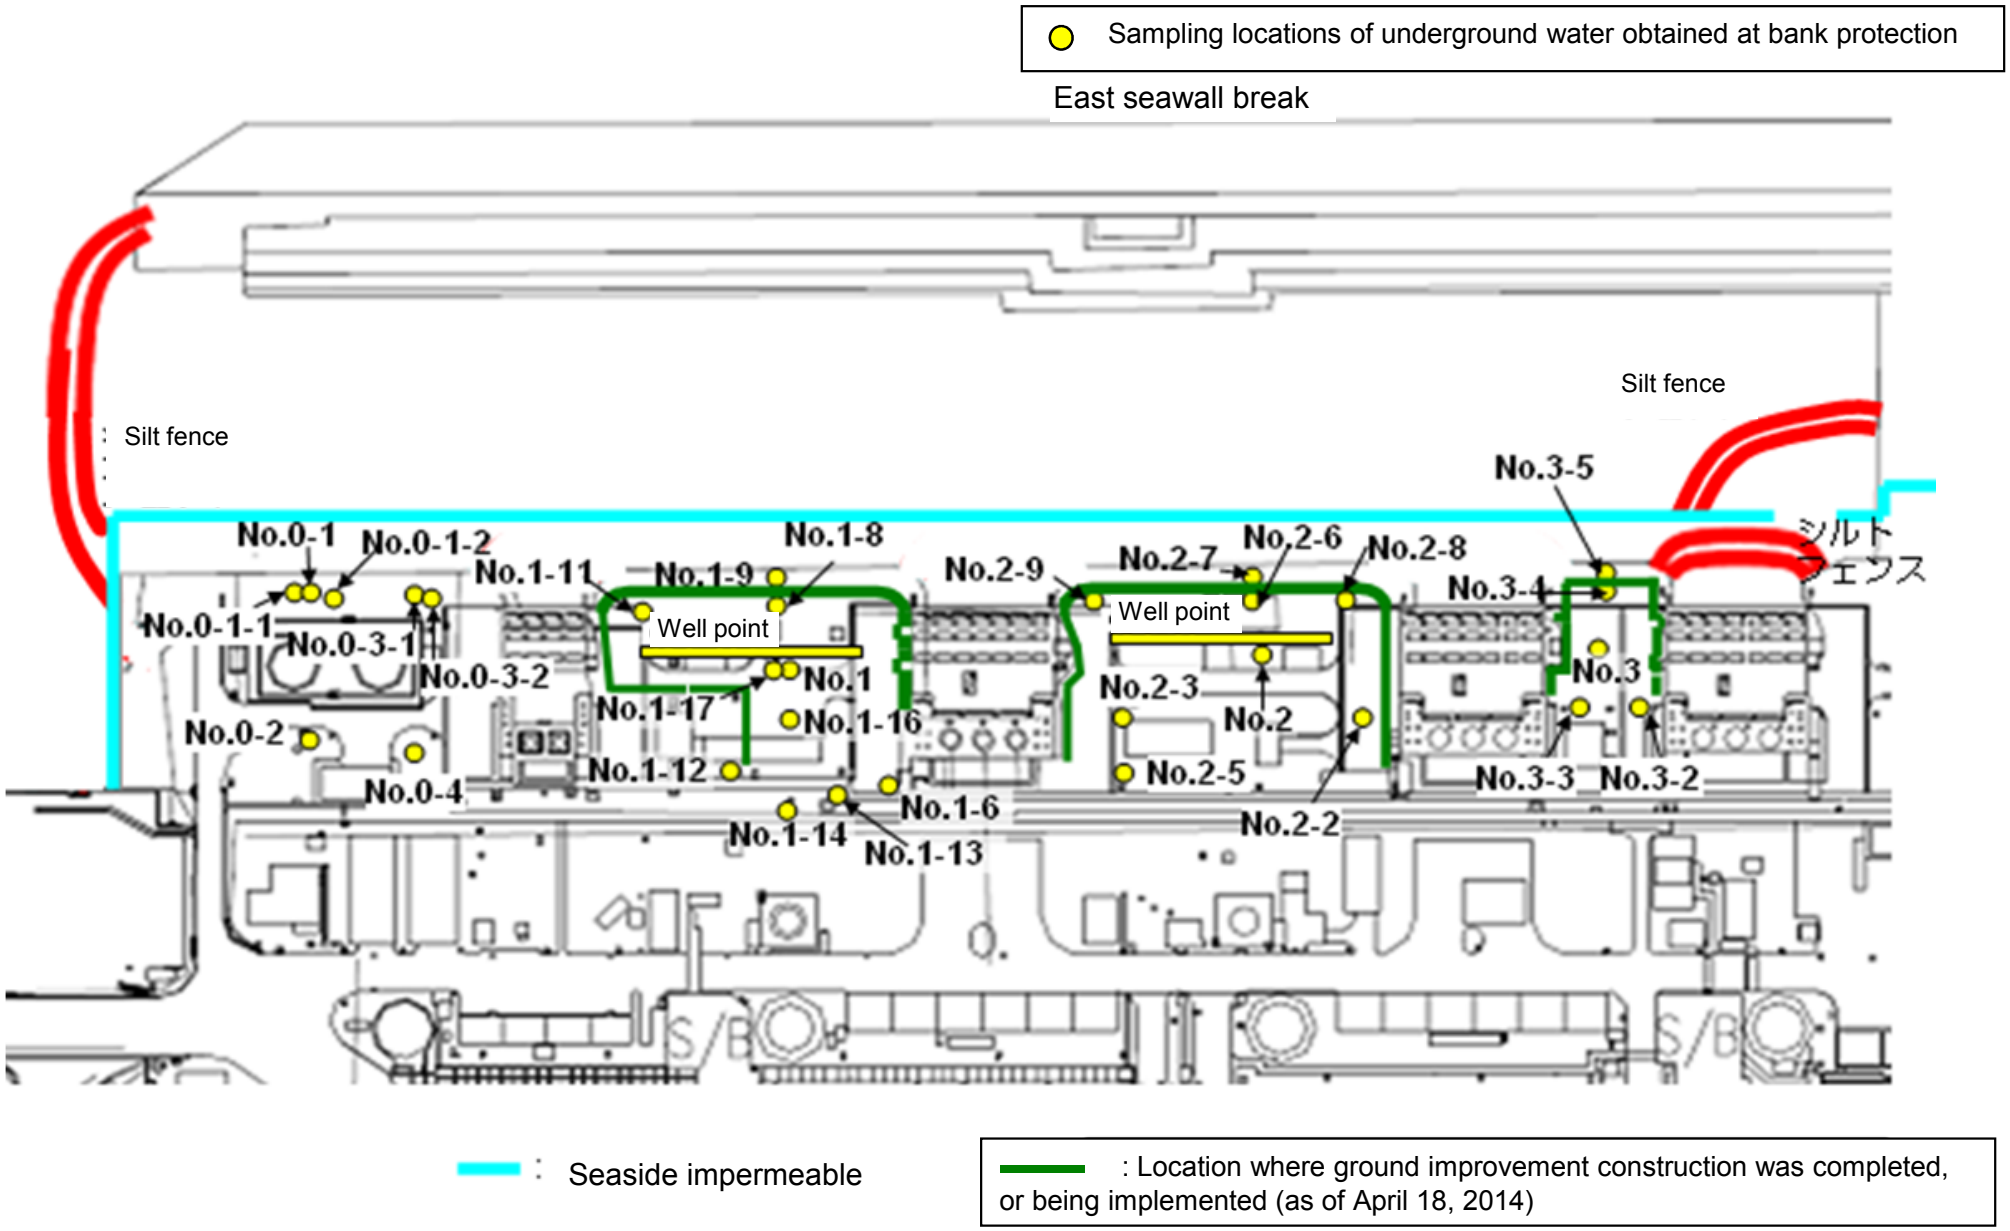

Detailed Analysis Results in the Port of Fukushima Daiichi NPS, around Discharge Channel and Bank Protection (1/2)
Underground Water Obtained at Bank Protection

Unit: Bq/L (exclude chloride)

	Underground water observation hole No.0-1	Underground water observation hole No.0-1-2	Underground water observation hole No.0-2	Underground water observation hole No.0-3-1	Underground water observation hole No.0-3-2	Underground water observation hole No.0-4	Underground water observation hole No.1	Underground water observation hole No.1-6	Underground water observation hole No.1-8	Underground water observation hole No.1-9	Underground water observation hole No.1-11	Underground water observation hole No.1-12	Underground water observation hole No.1-14	Underground water observation hole No.1-16	Underground water observation hole No.1-17
Date of sampling															
Time of sampling															
Chloride (unit: ppm)															
Cs-134 (Approx. 2 years)															
Cs-137 (Approx.30 years)															
The other γ															
Gross β															
H-3 (Approx. 12 years)															
Sr-90（Approx. 29 years）															

	Groundwater pumped up from the well point (between Unit 1 and 2)	Underground water observation hole No.2	Underground water observation hole No.2-2	Underground water observation hole No.2-3	Underground water observation hole No.2-5	Underground water observation hole No.2-6	Underground water observation hole No.2-7	Underground water observation hole No.2-8	Groundwater pumped up from the well point (between Unit 2 and 3)	Underground water observation hole No.3	Underground water observation hole No.3-2	Underground water observation hole No.3-3	Underground water observation hole No.3-4	Underground water observation hole No.3-5
Date of sampling							Jun 25, 2014							
Time of sampling							10:29 AM							
Chloride (unit: ppm)							880							
Cs-134 (Approx. 2 years)							ND(0.42)							
Cs-137 (Approx.30 years)							1.0							
The other γ														
Gross β							1,000							
H-3 (Approx. 12 years)							670							
Sr-90（Approx. 29 years）														

* Data announced this time is provided in a thick-frame. The other data was announced on June 26.
* "ND" indicates that the measurement result is below the detection limit, and the detection limit of each nuclide is provided in parentheses.
* "-" indicates that the measurement was out of range.

Detailed Analysis Results in the Port of Fukushima Daiichi NPS, around Discharge Channel and Bank Protection (2/2)
Underground Water Obtained at Bank Protection

Unit: Bq/L (exclude chloride)

	Underground water observation hole No.0-1	Underground water observation hole No.0-1-2	Underground water observation hole No.0-2	Underground water observation hole No.0-3-1	Underground water observation hole No.0-3-2	Underground water observation hole No.0-4	Underground water observation hole No.1	Underground water observation hole No.1-6	Underground water observation hole No.1-8	Underground water observation hole No.1-9	Underground water observation hole No.1-11	Underground water observation hole No.1-12	Underground water observation hole No.1-14	Underground water observation hole No.1-16	Underground water observation hole No.1-17
Date of sampling															
Time of sampling															
Chloride (unit: ppm)															
Cs-134 (Approx. 2 years)															
Cs-137 (Approx.30 years)															
The other γ															
Gross β															
H-3 (Approx. 12 years)															
Sr-90（Approx. 29 years）															

	Groundwater pumped up from the well point (between Unit 1 and 2)	Underground water observation hole No.2	Underground water observation hole No.2-2	Underground water observation hole No.2-3	Underground water observation hole No.2-5	Underground water observation hole No.2-6	Underground water observation hole No.2-7	Underground water observation hole No.2-8	Groundwater pumped up from the well point (between Unit 2 and 3)	Underground water observation hole No.3	Underground water observation hole No.3-2	Underground water observation hole No.3-3	Underground water observation hole No.3-4	Underground water observation hole No.3-5
Date of sampling							Jun 27, 2014							
Time of sampling							10:22 AM							
Chloride (unit: ppm)							870							
Cs-134 (Approx. 2 years)							ND(0.46)							
Cs-137 (Approx.30 years)							1.4							
The other γ														
Gross β							980							
H-3 (Approx. 12 years)							Under analysis							
Sr-90（Approx. 29 years）							-	-	-	-	-	-	-	-

* "ND" indicates that the measurement result is below the detection limit, and the detection limit of each nuclide is provided in parentheses.
* "-" indicates that the measurement was out of range.

<Reference> The Highest Dose Until the Previous Measurement (Groundwater Obtained at Bank Protection)

Unit: Bq/L

		Groundwater observation hole No.0-1	Groundwater observation hole No.0-1-1	Groundwater observation hole No.0-1-2	Groundwater observation hole No.0-2	Groundwater observation hole No.0-3-1	Groundwater observation hole No.0-3-2	Groundwater observation hole No.0-4	Groundwater observation hole No.1	Groundwater observation hole No.1-1*	Groundwater observation hole No.1-2*	Groundwater observation hole No.1-3*	Groundwater observation hole No.1-4*	Groundwater observation hole No.1-5*	Groundwater observation hole No.1-6
Cs-134 (Approx. 2 years)		29 <5/25>	ND	0.61 <3/2>	0.61 〔10/13〕	0.64 <4/6>	0.82 <1/14>	0.47 <6/22>	13 〔8/29〕	1.9 〔7/8〕	11,000 〔7/9〕	10 〔9/2〕	1.5 〔7/8〕	310 〔8/5〕	7,400 <6/16>
Cs-137 (Approx.30 years)		78 <5/25>	ND	1.5 <3/2>	2.2 <1/12>	1.1 <4/6>	2.1 <1/14>	1.4 <1/12>	31 〔8/29〕	3.6 〔7/8〕	22,000 〔7/9〕	24 〔9/2〕	3.6 〔7/8〕	650 〔8/5〕	20,000 <6/16>
The other γ	Ru-106 (Approx. 370 days)	ND	ND	ND	ND	ND	ND	ND	26 〔5/24〕	7.9 〔7/8〕	160 〔8/15〕	17 〔7/22〕〔8/8〕	3.1 〔8/8〕	ND	ND
	Mn-54 (Approx. 310 days)	ND	ND	ND	ND	ND	0.64 <2/20>	ND	ND	1.0 〔7/5〕	62 〔7/5〕	ND	ND	ND	320 <2/13> <2/17>
	Co-60 (Approx. 5 years)	ND	ND	ND	ND	ND	ND	ND	0.50 〔7/19〕	ND	3.1 〔7/8〕	ND	ND	ND	830 <2/20>
	Sb-125 (Approx. 3 years)	ND	ND	ND	ND	ND	ND	ND	1.7 〔7/11〕	ND	250 〔7/15〕	1.4 〔7/12〕〔8/26〕	ND	12 〔8/8〕	34 <5/19>
Gross β		300 [8/29] <5/18>	21 〔12/7〕	24 <6/22>	87 〔10/13〕	ND	67*1 〔12/11〕	44 <6/22>	1,900 〔5/24〕	4,400 〔7/8〕	9,300,000 〔7/8〕	160,000 〔8/12〕〔8/15〕	380 〔8/19〕	56,000 〔8/5〕	890,000 <6/19>
H-3 (Approx. 12 years)		45,000 〔8/29〕	18,000 〔12/7〕	74,000 [12/15] <1/19>	6,800 <2/16>	ND	76,000 <2/6>	56,000 <2/23>	500,000 〔5/24〕〔6/7〕	630,000 〔7/8〕	430,000 〔9/16〕	290,000 〔7/12〕	98,000 〔7/11〕	72,000 〔8/15〕	*2 110,000 <2/6>
Sr-90(Approx. 29 years)		140 〔8/8〕	7.9 〔12/7〕	2.6 〔11/10〕	0.73 〔9/2〕	1.5 〔11/20〕	2.3 〔12/6〕	ND(0.83) 〔10/27〕	1,300 〔8/22〕	2,300 〔6/28〕	5,000,000 〔7/5〕	130,000 〔8/8〕	200 〔7/8〕	5,100 〔8/22〕	-

Unit: Bq/L

		Groundwater observation hole No.1-8	Groundwater observation hole No.1-9	Groundwater observation hole No.1-10	Groundwater observation hole No.1-11	Groundwater observation hole No.1-12	Groundwater observation hole No.1-13	Groundwater observation hole No.1-14	Groundwater observation hole No.1-16	Groundwater observation hole No.1-17	Groundwater pumped up from the well point (between Unit 1 and 2)	Groundwater observation hole No.2	Groundwater observation hole No.2-1*	Groundwater observation hole No.2-2	Groundwater observation hole No.2-3
Cs-134 (Approx. 2 years)		47 〔11/25〕	170 〔9/3〕	-	1.1 <1/13>	74 〔10/21〕	37,000 <2/13>	88 *2 <2/27>	3.1 *1 〔12/13〕	1.3 <6/12>	110 〔9/23〕	0.88 <2/26>	0.66 〔9/1〕	15 <2/12>	2.2 <2/26>
Cs-137 (Approx.30 years)		110 〔11/25〕	380 〔9/3〕	-	3.4 <4/28>	170 〔10/21〕	93,000 <2/13>	230 *2 <2/27>	6.5 <6/26>	2.8 <4/28>	250 〔9/23〕	2.5 <2/26>	1.1 〔8/29〕〔9/1〕	38 <2/12>	5.5 <2/26>
The other γ	Ru-106 (Approx. 370 days)	ND	ND	-	ND	5.4 〔10/28〕	ND	ND	9.2 〔10/28〕	5.5 <4/21> <5/1>	25 〔9/2〕	ND	ND	ND	ND
	Mn-54 (Approx. 310 days)	12 <2/3>	ND	-	ND	ND	ND	0.4 <6/9>	ND	ND	8.5 <4/28>	ND	ND	ND	0.29 〔12/6〕
	Co-60 (Approx. 5 years)	1.3 <2/3>	ND	-	ND	0.51 〔10/24〕	ND	0.44 <5/29>	0.9 〔11/7〕	0.61 〔11/25〕	0.61 <6/9>	ND	ND	ND	ND
	Sb-125 (Approx. 3 years)	ND	ND	-	ND	61 〔10/21〕	ND	ND	24 <6/16>	2.1 〔11/25〕	ND	ND	ND	ND	ND
Gross β		59,000 <2/3>	2,100 *2 〔11/17〕	78 *2 <1/27>	2,300 〔12/26〕	1,100 <5/5>	260,000 <2/12> <2/13>	4,800 <6/9>	3,100,000 <1/20> <1/30> <2/3>	70,000 <6/26>	1,900,000 〔9/23〕	1,700 〔7/8〕	380 〔7/29〕	600 <4/16>	1,500 〔12/6〕 <1/8>
H-3 (Approx. 12 years)		33,000 <6/2>	860 *2 〔11/14〕	270,000 *2 <1/27>	85,000 〔9/13〕	440,000 〔10/31〕	88,000 <2/12>	23,000 <2/13>	43,000 〔9/26〕	32,000 <1/20>	460,000 〔8/19〕	1,000 <2/23>	440 〔8/26〕	660 <1/8>	1,700 〔12/6〕
Sr-90(Approx. 29 years)		20,000 〔12/9〕	300 〔10/3〕	—	18 〔10/21〕	290 〔10/21〕	Under analysis	98 〔12/9〕	1,400,000 〔12/9〕	9.5 〔12/9〕	—	54 〔5/31〕	5.9 〔7/25〕	320 〔12/25〕	1,200 〔12/6〕

Unit: Bq/L

		Groundwater observation hole No.2-5	Groundwater observation hole No.2-6	Groundwater observation hole No.2-7	Groundwater observation hole No.2-8	Groundwater observation hole No.2-9	Groundwater pumped up from the well point (between Unit 2 and 3)	Groundwater observation hole No.3	Groundwater observation hole No.3-1*	Groundwater observation hole No.3-2	Groundwater observation hole No.3-3	Groundwater observation hole No.3-4	Groundwater observation hole No.3-5
Cs-134 (Approx. 2 years)		41 <5/7>	17 <3/11>	3.5 <2/23>	0.47 <4/9>	ND	2.0 <4/23>	3.5 〔7/25〕	1.2 〔7/25〕〔8/8〕	14 <6/25>	130 <6/25>	3.9 <6/18>	64 <1/15>
Cs-137 (Approx.30 years)		110 <5/7>	50 <3/11>	9.0 <2/23>	1.3 <4/9>	0.58 *2 <2/11>	4.7 <4/23>	5.9 〔8/8〕	2.6 〔8/1〕	36 <6/25>	360 <6/25>	12 <6/11>	170 <1/15> <6/4>
The other γ	Ru-106 (Approx. 370 days)	ND	ND	ND	ND	6.5 *2 <2/11>	ND	ND	ND	ND	ND	ND	-
	Mn-54 (Approx. 310 days)	0.95 <6/4>	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.54 〔10/30〕	-
	Co-60 (Approx. 5 years)	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	-
	Sb-125 (Approx. 3 years)	74 <5/7>	ND	ND	ND	ND	ND	1.6 <1/1>	ND	ND	ND	ND	-
Gross β		150,000 <2/12>	3,200 〔12/5〕	1,300 <6/20>	4,400 <6/15> <6/22>	1,700 *2 <2/7>	240,000 〔12/12〕	1,400 〔7/11〕	180 〔8/1〕	2,800 *2 <5/28>	4,900 <4/30>	33 <6/11>	350 <5/28>
H-3 (Approx. 12 years)		7,900 <4/9>	1,200 〔11/24〕〔11/27〕	1,100 <1/19>	1,700 <4/6> <6/8>	13,000 *2 <2/7> <2/11>	6,300 <6/11> <6/15> <6/18>	3,200 〔2012/12/12〕	460 〔8/1〕	2,800 <5/14> <6/11>	8,000 <5/7>	170 〔9/18〕	170 <1/8>
Sr-90(Approx. 29 years)		Under analysis	Under analysis	ND(1.4) 〔11/21〕	Under analysis	Under analysis	-	8.3 〔2012/12/12〕	4.4 〔7/23〕	Under analysis	-	ND	-

● Since some samples are still under analysis, the highest dose of the Strontium-90 is among those previously announced.
*1 Analysis result of pumped water.
*2 The results are for a reference, since the water was highly turbid. (γ and Gross β were measured after filtration.)

* "ND" indicates that the measurement result is below the detection limit.
* Date of sampling is provided in parentheses. ( ): 2013, < >: 2014
* "*" is provided next to the name of the holes where the sampling could not be performed due to the chemical injection of ground improvement.
